



**Barry Davies LL.B (Hons)**  
**Solicitor/Cyfreithiwr**  
 Head of Legal and Democratic Services  
 Pennaeth Gwasanaethau Cyfreithiol a  
 Democraidaidd

To: Councillors: Nancy Matthews, N. Phillips, Michael Priestly,  
 Eryl Williams, Arwel Pierce, W. G. Roberts, Sharon Frobisher,  
 Meirion Hughes and Alex Aldridge

CS/NG

28 September, 2011

Nicola Gittins

01352 702345

[nicola.gittins@flintshire.gov.uk](mailto:nicola.gittins@flintshire.gov.uk)

Dear Sir / Madam

A meeting of the **NORTH WALES RESIDUAL WASTE JOINT COMMITTEE** will be held in the **SIAMBR ARFON, ARFON AREA OFFICE, PENRALLT, CAERNARFON, GWYNEDD, LL55 1BN** on **THURSDAY, 6 OCTOBER 2011** at **10.30a.m.** to consider the following items.

Yours faithfully

Democracy & Governance Manager

### **AGENDA**

1. **APOLOGIES**
2. **DECLARATIONS OF INTEREST**
3. **APPROVAL OF PREVIOUS MINUTES**
4. **MATTERS ARISING FROM PREVIOUS MEETING**

County Hall, Mold. CH7 6NA  
 Tel. 01352 702400 DX 708591 Mold 4  
[www.flintshire.gov.uk](http://www.flintshire.gov.uk)  
 Neuadd y Sir, Yr Wyddgrug. CH7 6NR  
 Ffôn 01352 702400 DX 708591 Mold 4  
[www.siryfflnt.gov.uk](http://www.siryfflnt.gov.uk)

The Council welcomes correspondence in Welsh or English  
 Mae'r Cyngor yn croesawau gohebiaeth yn y Cymraeg neu'r Saesneg

5. **PROGRESS REPORT (SO REPORT)**

6. **RIR – RISK STATUS UPDATE (SP REPORT)**

7. **COMMUNICATIONS UPDATE (SO REPORT)**

**LOCAL GOVERNMENT (ACCESS TO INFORMATION) ACT 1985 – TO  
CONSIDER THE EXCLUSION OF THE PRESS AND PUBLIC**

The following item is considered to be exempt by virtue of Paragraph(s) 14 of  
Part 1 of Schedule 12A of the Local Government Act 1972 (as amended)

8. **WASTE FLOW MODEL REPORT (SP REPORT)**

9. **ANY OTHER BUSINESS**



**NWRWTP**

North Wales Residual Waste Treatment Project

## **NORTH WALES RESIDUAL WASTE JOINT COMMITTEE**

Minutes of the meeting of the Joint Committee held in the Council Chamber,  
Bodlondeb, Conwy on Friday, 3 June 2011 at 10.30 am

### **PRESENT**

Councillor Eryl Williams – Denbighshire County Council (**Chair**)  
Councillor Mike Priestley – Conwy County Borough Council  
Councillor Meirion Hughes – Conwy County Borough Council  
Councillor Arwel Pierce – Gwynedd County Council  
Councillor Sharon Frobisher – Denbighshire County Council  
Councillor Neville Phillips – Flintshire County Council  
Alex Aldridge – Commissioner for the Isle of Anglesey County Council

### **ALSO PRESENT**

#### **Conwy County Borough Council**

Andrew Kirkham (Acting Corporate Director and Head of Financial Services)

#### **Denbighshire County Council**

Steve Parker (Head of Environment)

#### **Gwynedd County Council**

Dilwyn Williams (Corporate Director)

#### **Flintshire County Council**

Colin Everett (Chief Executive)  
Kerry Feather (Head of Finance)  
Louise Pedreschi (Solicitor)

#### **Isle of Anglesey County Council**

Arthur Owen (Corporate Director)  
Meirion Edwards (Chief Waste Management Officer)

#### **North Wales Residual Waste Treatment Project**

Stephen Penny (Project Director)  
Steffan Owen (Project Manager)

### **11. APOLOGIES**

Apologies for absence were received from Councillor Nancy Matthews (Flintshire County Council) and Barry Davies (Head of Legal and Democratic Services (Flintshire County Council))

### **12. MINUTES**

The minutes of the meeting of the North Wales Residual Waste Joint Committee held on 25 March 2011 were submitted for approval. Alex Aldridge stated that he was present in his capacity as a Commissioner for the Isle of Anglesey County Council and not as a County Councillor for Flintshire County Council. Mr Aldridge stated



# NWRWTP

North Wales Residual Waste Treatment Project

that he should not be referred to as Councillor in any future minutes.

Furthermore, Mr Aldridge had declared an interest at the last meeting as he was also a County Councillor for Flintshire County Council, a partner Local Authority for the NWRWTP.

## **RESOLVED-**

**That, subject to the above amendments, the minutes of the meeting of the North Wales Residual Waste Joint Committee held on 25 March 2011 be approved as a correct record.**

### **13. DECLARATIONS OF INTEREST**

Alex Aldridge, Commissioner for Isle of Anglesey, declared a personal interest as he was also a County Councillor for Flintshire County Council.

### **14. PROGRESS REPORT**

The Project Manager presented the progress report and stated that the project was progressing within budget and the final expenditure for 2010/11 was £867,431.71 which equated to £173,486.43 per Local Authority.

There were no major issues and an update with regard to minor issues in relation to the project activity was as follows:-

- ID 32 – Heads of Terms (HoTs) had been signed. Following concerns by the relevant Highways Authority regarding the proposed site at Anglesey Aluminium discussions were on-going to resolve those issues. A meeting had taken place with the landowner and it was hoped that all issues would be resolved by June 2011
- ID 42 – Meetings had been held with the Welsh Government (WG) in relation to possible funding stream for rail related projects. Feedback from Members on possible rail projects would be provided from the future NWRWTP workshops
- ID 59 – Apart from the Project Agreement all Invitations to Participate in Dialogue (ITCD) documentation had been issued
- ID 60 – Seven sessions had been held with participants to discuss waste transfer sites and waste related activities. All the technical issues would need to be completed before the project could move forward to discuss the commercial issues
- ID 61 – The latest waste flow figures had been issued and the waste flow model would be based on those latest figures. A report on those waste flow figures would be presented at the next meeting of the NWRWTP

In relation to the latest Westminster Government initiative to consider providing funding to Councils for a weekly bin collection



# NWRWTP

North Wales Residual Waste Treatment Project

this would not affect Wales. WG had their own powers to deal with waste collection and had given a clear indication that Wales would continue with a fortnightly collection. If a weekly bin collection was put forward by WG solutions, such as lowering the capacity of bins, would need to be explored.

- ID 70 – A report on Road/Rail Projects would be presented at a future meeting of the NWRWTP
- ID 71 – There potentially would be an early indication of the price of the waste treatment solutions in August 2011
- ID 78 – The second Inter Authority Agreement (IAA) would be commenced once the waste treatment solutions were known

## **RESOLVED-**

**That the progress report for the project be noted.**

### **15. RIR – RISK STATUS UPDATE**

The Project Director presented the Risk Register Report, which highlighted some of the amendments that had been made to reflect the current understanding of the risk and mitigation measures that are in place.

A risk had been identified in relation to the WG consultation on the new sector plans for Collections, Infrastructure and Market Sector Plan and Food, Manufacture, Service and Retail Sector Plan. Within the consultations reference is made to the possible introduction of a tax on waste to energy, although the documents acknowledge that at present WG did not have the power to do this. Following a response from WG it was acknowledged that this reference to a tax on waste energy was not formal policy and is likely to be removed from the Plans. However, until the final Sector Plans had been published this would remain a risk.

Members had no matters to raise in relation to the risks outlined in appendix 1, and the changes made during the period as outlined in appendix 2.

## **RESOLVED-**

**That the updated risk register for the project be noted.**

### **16. COMMUNICATION UPDATE**

The Project Manager updated Members with regard to the Communication matters concerning the NWRWTP.

A press release had been issued announcing that the project was in discussion with Anglesey Aluminium regarding securing a portion of the site for the project. A Members' Newsletter had also been released with the same information.

Members were presented with a draft consultation booklet for their



# NWRWTP

North Wales Residual Waste Treatment Project

comment. Once finalised the booklet would be printed and circulated to relevant locations such as Council Offices, libraries and leisure centres etc.

Member Sessions would be held on Friday, 17 June 2011 at 2.00 pm in Bangor and on Wednesday, 29 June 2011 at 2.00 pm in St Asaph. As only a handful of Members had confirmed their attendance at the sessions it was suggested that an invitation reminder be sent out as soon as possible.

Comments and answers to Member queries were as follows:-

- Customer feedback had already been obtained, however, the consultation would provide the evidence needed to support any Planning Applications related to the Project. Furthermore, a number of options would be provided for the Project and the consultation could influence the solution
- The Workshop Sessions would be facilitated by the Project Manager, Project Director and John Twitchen of Sauce Consultancy
- In relation to consulting the project the following options were suggested:-
  - Drop-in Sessions
  - Road shows at Supermarkets and Shopping Centres
  - Telephone Surveys
  - Workforce via the relevant partner Intranets
  - Workforce of Partner Organisations such as the Snowdonia National Park, North Wales Fire and Rescue Service, North Wales Police and Betsi Cadwaladr University Health Board via their websites

In relation to concerns regarding Members' predetermining a Planning Application through their role as an Elected Member, suitable advice should be given to Members at Workshops. Furthermore, a letter should be sent with the consultation to Members. Members should be reminded that if they used their role as a Local Electoral Division Member to voice their concerns publically this would be considered as pre-determination and therefore they would be debarred from any Planning Committee decision.

#### **RESOLVED-**

- (a) **That the circulation of the Press Release and Members' Newsletter be noted.**
- (b) **That the consultation booklet be approved.**
- (c) **That a reminder invitation be circulated to Members regarding the Workshop Sessions.**
- (d) **That a letter be sent to all Members, with the consultation booklet, providing advice in relation to pre-determination.**

## **17. PROCUREMENT RAIL UPDATE**



# NWRWTP

North Wales Residual Waste Treatment Project

To Project Director updated Members on the proposed approach for considering the potential adoption of rail as part of the NWRWTP solution within the procurement process.

The Partnership made it clear to Participants, throughout the procurement process to date, that the Partnership wanted to explore the potential use of rail as part of any solution that may be developed for the Project.

Following discussion within the project team, and its external legal advisors, a process was recommended that posed a low risk of challenge, and still enabled the Partnership to make a policy decision on whether it desired a road or rail based solution at the appropriate stage.

In brief the process was:-

- Invitation to Submit Detailed Solutions (ISDS) stage Participants required to submit fully developed road and rail solutions in September 2011
- Partnership to assess both the submissions and decide on a road or rail solution at Joint NWRWTP Committee meeting to be held in October 2011. No participants would be de-selected at this stage
- Participants informed of the Partnerships' decision (road or rail based solution) and given a further 3 weeks to refine their solution (via an Invitation to Submit refined solutions - ISRF)
- Participants' ISRF responses submitted in November 2011 with the Partnership making its decision on the two Participants to be taken through to the CFT stage in January 2012
- The two stage process extended the procurement process by up to a period of 3 months, but it was the view of the project team that this additional stage was required to ensure rail can be appropriately considered

The Project Director was confident that following an initial assessment regarding network access Participants would be able to deliver a rail submission. Members were further advised that Anglesey Aluminium already had a rail head located at the site.

## **RESOLVED-**

**That the proposed procurement approach to enable the Partnership to determine its policy preference in relation to the use of road or rail as the basis for solutions be approved.**

## **18. ANY OTHER BUSINESS**

Members were advised that Friends of the Earth had issued a briefing



# NWRWTP

North Wales Residual Waste Treatment Project

statement. A response to that statement had been sent to ENTEC for their technical input. The response would be sent to Members for their comment but a reply was required by the morning of Monday, 6 June 2011 to enable the response to be issued by the afternoon of that day.





## AGENDA ITEM NUMBER 5

### **NORTH WALES RESIDUAL WASTE TREATMENT PROJECT PROGRESS REPORT**

#### **NORTH WALES RESIDUAL WASTE JOINT COMMITTEE**

**Date : 6 October 2011**

**Period: 26 May 2011 to 28 September 2011**

#### **PROJECT SUMMARY**

To procure a sustainable waste management solution for the 5 local authorities in North Wales (Conwy, Denbighshire, Flintshire, Gwynedd and Isle of Anglesey) that will assist with the reduction in greenhouse gas emissions from landfill and will minimise the tonnage of waste residue sent to landfill thus ensuring that the authorities avoid Landfill Allowance Scheme (LAS) infraction penalties and meet National Waste Strategy targets.

#### **PROJECT STATUS**

<b>Overall Project Status</b>	
<b>Amber</b>	<p>Dialogue has been continuing with the three participants on legal, financial and technical matters. The consultation process has progressed with various sessions held across the Partnership area for stakeholders and the public to discuss the project.</p> <p>Extension of time for ISDS submission requested by one participant to the timetable.</p>

<b>Budget status</b>	
<b>Green</b>	<p>Actual spend for this financial year up to 19/08/11 is £312,096.</p> <p>Profiled spend for this financial year up to 31/07/11 is £405,087. (Under profile by £92,991).</p>

<b>Status</b>	<b>Meaning</b>
<b>Green</b>	There are no problems; all is progressing well and to plan
<b>Amber</b>	There are some minor/ less significant problems. Action is needed in some areas but other parts are progressing



	satisfactory
<b>Red</b>	There are significant problems and urgent and decisive action is needed.

**PROJECT UPDATE** – Activities due for completion 26<sup>th</sup> May 2011 to 28<sup>th</sup> September 2011 (and highlighted longer term actions).

ID	Activity	RAG status	Comments	Forecast	Actual
32	Option developed on second site that is capable of acceptance by Joint Committee	Amber	Verbal update by Project Director.	May 2011	
60	Identify issues with potential use of existing sites arising from ISOS submissions	Green	Extensive dialogue held with all bidders on sites. General agreement reached with each bidder.	September 2011	Complete
61	Liaise with technical officers on waste flows following 2010/11 outturn data.	Green	Individual sessions held between Amec and the individual authorities to go through waste flow models in detail. Technical group session held to agree waste flow forecast. See item 8 on Agenda	June 2011	Complete
62	Procure advisors to plan and carry out consultation exercise on approach of partnership	Amber	Consultation process began in June 2011	End Feb 2011	Complete
63	Decide on engagement and facilitation support	Amber	Facilitation support used on an as and when required basis. Sauce Consultancy for specialist strategic advice and support.	March 2011	Complete
64	June Dialogue sessions	Green	Meetings with participants as part of competitive dialogue process	June 2011	Complete
65	July Dialogue sessions	Green	Meetings with participants as part of competitive dialogue	July 2011	Complete



# NWRWTP

North Wales Residual Waste Treatment Project

			process		
66	August Dialogue sessions	Green	Meetings with participants as part of competitive dialogue process	August 2011	Complete
67	September Dialogue sessions	Green	Meetings with participants as part of competitive dialogue process	September 2011	Complete
68	Briefing pack provided to minerals and waste planning officers	Green	Briefing pack provided to Planning Officers	June 2011	Complete
69	Issue ISDS Waste Flow Model to participants	Amber	Following action 61	End of June 2011	Complete
70	Process for assessment of road / road-rail solutions to be determined	Green	Process for assessment of road/ rail solutions agreed.	July 2011	Complete
71	Project Team to receive early indications of content of potential ISDS submissions including pricing information etc	Green	To aid internal project team and partner authority Finance Officers such that there are no “surprises” when ISDS submissions are ultimately received.	August 2011	Complete
72	ISDS solutions to be submitted by participants	Amber	Verbal update by PD at meeting (see Appendix 1 below for revised procurement timetable)	Late January 2012	
73	Assessment of ISDS submissions	Amber	Key information provided to Finance, Technical and Legal Officers prior to developing recommendations to Project Board and Joint Committee	February 2012	
74	Participants informed of partnership’s decisions on road / road-rail, and invited to submit	Amber	As per revised procurement timetable (see Appendix 1)	Early March 2012	



# NWRWTP

North Wales Residual Waste Treatment Project

	refinements to their ISDS submissions in the light of decision				
75	Submission of Refined ISDS by participants	Amber	As per revised procurement timetable (see Appendix 1)	Apr / May 2012	
76	Refined ISDS submissions evaluated	Amber	As per revised procurement timetable (see Appendix 1)	May / June 2012	
77	Negotiation positions to be agreed by Project Board	Green	The PD will develop a number of “best” and “backstop” positions for approval by the Project Board, that will be used to take commercial positions within the procurement process	July 2011	Complete
78	The second IAA (IAA2) to be commenced	Green	This to commence once ISDS solutions are known (and the likely contract structures are more certain). Some preliminary discussions and development work to be carried out during summer 2011.	November 2011	
79	Partnership sites title information and related constraints gathered and identified	Green	Title information received. See action 82 below.	June 2011	Complete
80	Project Team and Lead Legal Officer to meet with Estates to discuss any inconsistencies in the title information	Green		4 October 2011	
81	Additional period given for consultation responses	Green	Two weeks added to allow for last minute / late responses in the interest of including as	7 October 2011	



# NWRWTP

North Wales Residual Waste Treatment Project

			many responses as possible		
82	Full analysis of consultation responses	Green	Report to be drawn up showing results of consultation exercise	October 2011	
83	Report back to public and respondents with results of consultation	Green	TBC (see item 86 below)	TBC	
84	Communication and engagement plan for next 12 months	Green	Meeting organised with Project Team, Amec and Sauce Consultancy to plan communication and engagement going forward for the next 12 months	21 October 2011	
85	Meet Environment Agency Wales to discuss technical issues arising from proposals	Green		November 2011	
86	Further dialogue sessions prior to ISDS submissions	Green		December 2011	
87	Financial and technical teams to be consulted on the road / rail assessment result prior to Project Board and Joint Committee	Green		February 2012	
90	Road / Rail assessment results to be presented to Project Board and Joint Committee	Green		February / March 2012	



# NWRWTP

North Wales Residual Waste Treatment Project

**KEY RISKS** – See item 6 on this agenda.

## Appendix 1 – Outline Procurement Timetable

Key

Joint Committee decision	Individual partner authority decision	WG Review / Decision
--------------------------	---------------------------------------	----------------------

### Key Decision Points

Stage	Key dates	Key decision	Who
Joint Committee - road/ rail	March 2012	Decision on road/ rail	JC (finance officers consulted )
Joint Committee ISDS de-selection	21/06/2012	De-selection of 1 participant	JC
WG Readiness review	Sep to Oct 2012	Are all issues resolved before dialogue can be closed ?	WG
Joint Committee approve preferred bidder, FBC and IAA2	Feb 2013	Preferred bidder, FBC and IAA2	JC
Individual authority approve preferred bidder, FBC, IAA2 & authority to proceed to Contract award approvals	Feb to May 2013	Approved bidder, FBC, IAA2 & authority for JC to proceed to Contract award	Partner authorities (cabinet, scrutiny, full council etc)
Gateway review 3 – Investment Decision (WAG approval of FBC)	May to June 2013	Approval of funding	WG
JC approval of Contract award	Aug 2013	Contract award	JC
Planning application submitted for key facility	July 2013		
Planning determination	July 2013 to March 2014	Planning determination	Host authority(s) planning and regulatory committees



# NWRWTP

North Wales Residual Waste Treatment Project

Stage	Updated timetable	
	from	to
<b>ISDS submission</b>		<b>27/01/12</b>
<b>Joint Committee - road/ rail</b>		March 2012
Submission of refined ISDS		30/03/2012
<b>Joint Committee ISDS de-selection</b>		21/06/2012
WG Readiness review (assessment of readiness to close dialogue)	14/09/2012	25/10/2012
Submission of CFT		Jan2013
<b>JC approve preferred bidder &amp; FBC</b>		Feb 2013
<b>Individual authority approved bidder, FBC, IAA2 &amp; authority to proceed to Contract award approvals</b>	Feb2013	May 2013
<b>Approved bidder appointed</b>		May 2013
<b>Gateway review 3 – Investment Decision (WG approval of FBC)</b>	May 2013	June2013
Commercial close		June 2013
<b>JC approval of Contract award</b>		Jul-2013
<b>Contract Award</b>		Aug 2013
<b>Planning application submitted for key facility</b>		Jul 2013
Planning Consent achieved		Mar 2014
Construction period	Sep 2014	Dec 2016
Commissioning	Dec 2016	Mar 2017
<b>Facility fully available</b>		Mar 2017*

\*Note original OBC full facility availability was estimated at September 2016





# NWRWTP

North Wales Residual Waste Treatment Project

## AGENDA ITEM NO: 6

**REPORT TO: NWRWTP JOINT COMMITTEE**

**DATE: 6 OCTOBER 2011**

**REPORT BY: PROJECT DIRECTOR**

**SUBJECT: RISK REGISTER REPORT**

### **1. PURPOSE OF REPORT**

- 1.1. The members of the NWRWTP Joint Committee have requested that they are provided with an update of the risk register at each meeting of the Joint Committee.
- 1.2. This report will highlight some of the amendments to the risk register that have been made to reflect the current understanding of risks and mitigation measures that are in place.

### **2. BACKGROUND**

- 2.1. The Risk Register will require continual update throughout the project.

### **3. CONSIDERATIONS**

- 3.1. There is one new risk identified this reporting period.
  - PS 12 (Planning and Permitting). The recent issue of the draft Collections, Infrastructure and Markets Sector Plan (CIM) by WG has led to uncertainty as to the status of the existing Regional Waste Plan (RWP). The RWP may be given reduced weight in determination of a planning application for waste facilities if uncertainty remains over its status. The Project team and North Wales regional waste planning team are engaging with WG on this issue to ensure that the final issued version of Collections, Infrastructure and Markets Sector Plan (CIM) does not leave a planning "policy vacuum".
- 3.2. There is a change to existing risk F2 (finance) this period (Procurement delays lead to increased procurement costs due to extended procurement process). This is due to request from participants and extension to the ISDS timetable given (approx 5 months). The new timetable will still be within 12 month delay sensitivity produced for OBC.
- 3.3. The Top 9 risks (after controls have been put in place) are shown in appendix 1.
- 3.4. Risk TB4 closed as a duplicate of F2
- 3.5. The changes this period are shown in appendix 2.



# NWRWTP

North Wales Residual Waste Treatment Project

3.6. The risk register will continue to be reviewed by the Project Director and reported to the Project Board at future meetings.

#### **4. RECOMMENDATIONS**

4.1. That the Joint Committee note the updated risk register for the project.

#### **5. FINANCIAL IMPLICATIONS**

5.1. Not applicable

#### **6. ANTI-POVERTY IMPACT**

6.1. None

#### **7. ENVIRONMENTAL IMPACT**

7.1. Not applicable

#### **8. EQUALITIES IMPACT**

8.1. Not applicable

#### **9. PERSONNEL IMPLICATIONS**

9.1. Not applicable

#### **10. CONSULTATION REQUIRED**

10.1. Not applicable

#### **11. CONSULTATION UNDERTAKEN**

11.1. Not applicable

### **LOCAL GOVERNMENT ACCESS TO INFORMATION ACT 1985**

#### **Background Documents:**

None

**Contact Officer:** Stephen Penny NWRWTP



## Appendix 1 Top (Red) risks and issues

ID	Risk / Issue (i.e.: Threat to the Project)	Consequence	Current Assessment			How the risk will be managed and controlled		Residual risk after			Impln Date	Review Date	Additional explanatory notes
			Impact	L'hood	Overall	Already in Place	Not in Place (Proposed)	Impact	L'hood	Overall			
<b>Policy &amp; regulatory Risk – Change in WG objectives / regulations</b>													
PO1	WG changes financial support available for residual waste treatment projects due to WG affordability / budgetary constraints in the current economic climate	Residual waste treatment projects become less affordable for partnership and each partner authority	5	4	20	Project Team to monitor WG positions in terms of budget availability and lobby at ministerial level if there are indications that proposed funding is to be reduced		5	3	15	Ongoing	Nov-10	
PO2	WG Environmental policy and objectives change	Project is now inappropriate	4	5	20	Keep in close contact with WG to ensure potential policy changes that may impact on the project are identified early. Project team develop a partnership consultation response (for approval by the PB and Joint Committee) highlighting the potential impact of such a target on the project and to ensure WG addresses how any such target is related to potential household numbers of population growth rates that authorities may be subject to in future.		4	4	16	Ongoing	Feb-11	WG have indicated in the final Municipal Sector Plan (MSP) that they may adopt a waste minimisation target for MSW with a negative growth rate (reduction) of -1.2% pa. The WG MSP does not take any account of individual or partner authority HH or population growth rates. The Partnership has however received guidance from WG that the Partnership is free to make its own assessments about future waste arisings and as a result planning risk is now moderated.
PO4	Change in legislation or guidance either at European, National or Regional/Local level	Could require revisit of preferred solution, possible termination of project, excessive LAS compliance costs	3	5	15	Keep in close contact with WG to ensure potential policy changes that may impact on the project are identified early. Lobby WG and liaise with W/LGA on this issue.		3	4	12	Ongoing	Sep-10	WG have now clarified the position on use of IBA (Bottom ash) so the likelihood of policy change in relation to this has reduced. However recent sector plan consultations have raised the potential for the introduction of a tax on waste to energy. The Project team one of a number of options that WG may consider. If WG were to introduce such tax the financial impacts cannot be determined at this point but could potentially be considerable. (dependant on whether this would apply to household waste or just to C&I wastes). To be prudent the impact assement has been increased from 3 to 4 to reflect this uncertainty. The Project team have submitted a joint letter in conjunction with project green to WG. The Project team are now awaiting final publication of the Collections and Infrastructure Plan.



## Appendix 1 Top (Red) risks and issues (continued)

ID	Risk / Issue (i.e.: Threat to the Project)	Consequence	Current Assessment			How the risk will be managed and controlled		Residual risk after			Impln Date	Review Date	Additional explanatory notes
			Impact	L'hood	Overall	Already in Place	Not in Place (Proposed)	Impact	L'hood	Overall			
<b>Communication &amp; stakeholders – failure to proactively engage with key stake holders leading to delays and lack of public support for the proposed solution.</b>													
CO4	Pressure from lobby groups/public against the preferred solution and location.	Alternative solution/site has to be sought, increased project development costs, delays to project delivery programme, excessive LAS costs.	4	5	20		Project team will ensure an adequate stakeholder engagement and communications plan in place. Alternative site work will continue during early stages of procurement process.	4	3	12	Ongoing	Sep-10	
<b>Procurement Strategy and Process</b>													
P13	Technological solutions offered are not commissionable within LAS infraction timescales	LA' s face infraction fines for additional landfill above allowance	4	4	16	OBC modelling has shown that each partner authority can meet LAS allowances if they increase "front end" recycling and composting" and the project is delivered to timetable. Any underperformance in this "front end" recycling and composting are outside the scope of this project and any	Procurement process to ensure that is delivered in timely manner with the risk of late delivery of the residual waste treatment service minimised.	4	3	12	Ongoing	Sep-10	
<b>Planning and permitting –ability to secure successful planning and permitting outcome for solution</b>													
PS5	Suitable sites are not in council ownership to support development of the solution	Project delayed whilst suitable sites are secured	5	3	15	Project team are identifying sites that could be suitable for location of both the waste transfer stations and residual waste treatment facility(s)	Commence negotiations with land owners of (further) additional sites identified as potentially suitable for location of facilities with the aim of securing	5	3	15	Ongoing	Sep-10	
PS14	The recent issue of the draft Collections, Infrastructure and Markets Sector Plan (CIM) by WG has led to uncertainty as to the status of the existing Regional Waste Plan (RWP). Thus the RWP may be given reduced weight in determination of a planning application for waste facilities. A policy vacuum may therefore exist if this is not addressed by WG.	Unsuccessful planning application	4	4	16	Project team and north wales regional waste planning team engaging with WG on this issue to ensure that the final issued version of Collections, Infrastructure and Markets Sector Plan (CIM) does not leave a planning "policy vacuum".		4	3	12	Ongoing	Sep-11	WG's published draft Collections, Infrastructure and Markets Sector Plan (CIM) indicates that RWP's will be replaced but with no indication as to timetable for replacement.



## Appendix 1 Top (Red) risks and issues (continued)

ID	Risk / Issue (i.e.: Threat to the Project)	Consequence	Current Assessment			How the risk will be managed and controlled		Residual risk after			Impln Date	Review Date	Additional explanatory notes
			Impact	L'hood	Overall	Already in Place	Not in Place (Proposed)	Impact	L'hood	Overall			
<b>Wastes</b>													
W3	Composition of waste is different from that anticipated (poor data, policy changes, changes in collection practices)	Performance is below required level, excessive LAS compliance costs	3	5	15		Waste composition to be monitored during procurement and data shared at Competitive Dialogue to inform solution. All Wales Waste composition analysis being delivered by WG through WRAP. Initial work commencing in June 09. Performance of technology solution will be tested and understood as part of the procurement process to identify	3	4	12	Ongoing	Sep-10	Technology specific. EfW less sensitive to waste compositional change.
<b>Performance</b>													
PE1	Market/outlet is not available for outputs from the facility(s)	Increased project operational costs, increase in demand for landfill void	4	4	16		Ensure market deliverability demonstrated as part of procurement evaluation process.	4	3	12	Ongoing	Sep-10	Electricity sound, ash uncertain. Project and market saturation dependant.



# NWRWTP

North Wales Residual Waste Treatment Project

## Appendix 2 Headline Changes this Period

IDENTIFYING THE RISK or ISSUE						MANAGING THE RISK or ISSUE									Additional explanatory notes
ID	Risk / Issue (i.e.: Threat to the Project)	Consequence	Current Assessment			How the risk will be managed and controlled			Residual risk			Impln Date	Review Date	Clousre Date	
			Impact	L'hood	Overall	Already in Place	Who is Managin g	Not in Place (Proposed)	Who will Manage	Impa ct	L'ho od				
<b>Policy &amp; regulatory Risk – Change in WG objectives / regulations</b>															
PO4	Change in legislation or guidance either at European, National or Regional/Local level	Could require revisit of preferred solution, possible termination of project, excessive LAS compliance costs	4	5	20	Keep in close contact with WG to ensure potential policy changes that may impact on the project are identified early.	PD	Lobby WG and liaise with WMLGA on this issue.	PD	4	3	12	Ongoing	Sep-11	WG have now clarified the position on use of IBA (Bottom ash) so the likelihood of policy change in relation to this has reduced. However recent sector plan consultations have raised the potential for the introduction of a tax on waste to energy. The Project team one of a number of options that WG may consider. If WG were to introduce such tax the financial impacts cannot be determined at this point but could potentially be considerable. (dependant on whether this would apply to household waste or just to C&I wastes). To be prudent the impact assesment has been increased from 3 to 4 to reflect this uncertainty. The Project team have submitted a joint letter in conjunction with project green to WG. The Project team are now awaiting final publication of the Collections and Infrastructure Plan.
<b>Planning and permitting -ability to secure successful planning and permitting outcome for solution</b>															
PS14	The recent issue of the draft Collections, Infrastructure and Markets Sector Plan (CIM) by WG has led to uncertainty as to the status of the existing Regional Waste Plan (RWP). Thus the RWP may be given reduced weight in determination of a planning application for waste facilities. A	Unsuccessful planning application	4	4	16	Project team and north wales regional waste planning team engaging with WG on this issue to ensure that the final issued version of Collections, Infrastructure and Markets Sector Plan (CIM) does not leave a planning "policy vacuum".			PD	4	3	12	Ongoing	Sep-11	WG's published draft Collections, Infrastructure and Markets Sector Plan (CIM) indicates that RWP's will be replaced but with no indication as to timetable for replacement.
<b>Finance &amp; Affordability</b>															
F2	Procurement delays lead to increased procurement costs (due to extended procurement process)	LA's seek additional funding or withdraw	3	3	9	Affordability envelope has been agreed that includes delay to the project	PD	Manage procurement delays by appropriate design of procurement process.	PD	3	3	9	Jan-10	Sep-11	Due to request from participant and extension to the ISDS timetable given (approx 5 months). Timetable will still be within 12 month delay sensitivity produced for OBC.



# NWRWTP

North Wales Residual Waste Treatment Project

## AGENDA ITEM NO: 7

**REPORT TO: NWRWTP JOINT COMMITTEE**

**DATE: 6 OCTOBER 2011**

**REPORT BY: PROJECT MANAGER**

**SUBJECT: COMMUNICATIONS UPDATE**

### **1. PURPOSE OF REPORT**

- 1.1. To update the NWRWTP Joint Committee on communication matters concerning the North Wales Residual Waste Treatment Project (NWRWTP).

### **2. BACKGROUND**

- 2.1. The Joint Committee has requested regular updates on communication matters relating to the NWRWTP. This report provides an update on progress to date.

### **3. CONSIDERATIONS**

#### **3.1. Consultation Exercise - Summary**

The consultation exercise has been on going since the Member sessions were held in June 2011.

The closing date for consultation responses was Friday 23<sup>rd</sup> September, however the Project Team are including responses included for two weeks following this date in order to include as many responses as possible in the results. This was advertised in a press release that was issued on the 16 September 2011.

This means that a full report on the results of the consultation process will follow this report, however it was felt that an early indication of the results would be of benefit to the Joint Committee, therefore please note that the information below is an early indication and a summary of the results thus far only.

Below is a brief list of the activities that have taken place:-

- Two Member sessions were held (one “west” in Bangor, and one “east” in St Asaph)
- “Drop in” sessions at each of the five partner authorities (where members of the public were able to have an informal discussion about the project)
- Community Group sessions where various community groups etc were invited to attend a meeting to discuss the project and the consultation.



# NWRWTP

North Wales Residual Waste Treatment Project

- 2 interest group sessions where environmental / interest groups were invited to discuss the project (1 x east and 1 x west).
- The consultation questionnaire can be complete on line, and project website has a consultation page.
- The consultation has been advertised internally within the five partner authorities, including booklets distributed to Council Offices, libraries etc.
- A telephone survey of the consultation questionnaire commissioned of 1,000 residents of the partnership area.

### Member sessions

Two Member sessions were held on the 17<sup>th</sup> and 28<sup>th</sup> of June 2011. One “west” session in Bangor (Parc Menai), and one “east” session in St Asaph (Optic).

General feedback from the sessions is that they were a success, in particular the aspect of the Members of partner authorities meeting together. Appendix 3 shows the attendance for both sessions, followed by a brief list of the questions that were asked during the sessions.

### Drop in sessions

These were advertised in the local press / media through an advert in all the local press across the five authorities, together with a series of press releases. They were also advertised on the project website. As expected, turnout was low at the authorities where sites have not been mentioned as potentially hosting a facility.

- Conwy - 13
- Gwynedd (Dolgellau and Bangor) - 6
- Anglesey - 23
- Denbigh - 6
- Flintshire - 49 (27 at St David's Park, 22 at Connah's Quay Town Council)

Total attendance = 97

Below is a brief summary of the discussions held at the sessions

- Most of the discussions held were detailed, with some lasting over an hour. These were valuable and in depth discussions.
- The vast majority left the sessions happier than when they arrived, although there was a number that even after the discussions were against certain proposals (e.g. EfW at Anglesey or EfW at Deeside Industrial Park)
- In Gwynedd, Anglesey, Conwy and Denbighshire the vast majority of attendees were supportive of the project, and wanted to know more about it.
- In Flintshire, there was a greater concern about the possibility of an “incinerator at Deeside”, mainly centred around health effects. There is a lack of trust in the permitting and licensing regime from those that were opposed.
- It should be noted, though, that while a good number of the Flintshire drop in sessions' attendees had concerns, it was by no means universal, and indeed a good proportion were either





# NWRWTP

North Wales Residual Waste Treatment Project

supportive, or could recognise the arguments being made for both need, and why the site was being considered.

- It did not come across at any of the sessions that there is a groundswell of opposition to the project.

### Community Group sessions

The Community Group and interest group sessions were not well attended at all, with some sessions with one or two attendees. This is despite follow up calls to the invitees. In total, 12 people attended 5 sessions.

Overall, however, feedback was very positive at those sessions, with nearly all attendees supportive of the project. The sessions did, however, provide a good opportunity for detailed discussion, and also provided vital contacts for further consultation and engagement in the future.

### Summary of various “drop in” and community group sessions

Overall, whilst the attendance at some of the various sessions was disappointing, the project team has learnt a great deal from the sessions, and has had detailed discussions with a good number of residents, and opened up further avenues for engaging (more community groups identified etc).

The process has also highlighted the importance of a pro active engagement campaign throughout the procurement process, and it is clear that an informal detailed discussion with a resident has a far greater effect than more formal communications avenues (e.g. press releases etc)

### 3.2. Press Coverage

Face to face briefings were given to some of the local press during July in order to advertise the consultation process, and three press releases were issued during August and September advertising the drop in sessions and the closing date for consultation responses. There was reasonable press / media coverage during the consultation process and all the local press / media ran at least one story of some sort advertising the sessions (including BBC news website, Real Radio interview etc). Some ran a number of stories on the consultation. See appendix 2 below for some examples of the coverage.

### 3.3. Consultation Questionnaire – indication of results

In appendix 1 below are some graphs showing an early indication of the results thus far. The number of consultation responses received thus far is 305 (162 booklets, 143 via the on line questionnaire).

### 3.4. Communication and Engagement planning

The Project Team have arranged a meeting with technical and communication advisors on 21 October 2011 to plan communication and



# NWRWTP

North Wales Residual Waste Treatment Project

engagement going forward for the following 12 months. This will be put before the Joint Committee for approval once it is finalised.

#### **4. RECOMMENDATIONS**

4.1. To note the content of this update report.

#### **5. FINANCIAL IMPLICATIONS**

5.1. Not applicable.

#### **6. ANTI-POVERTY IMPACT**

6.1. Not applicable.

#### **7. ENVIRONMENTAL IMPACT**

7.1. Not applicable.

#### **8. EQUALITIES IMPACT**

8.1. Not applicable .

#### **9. PERSONNEL IMPLICATIONS**

9.1. Not applicable.

#### **10. CONSULTATION REQUIRED**

10.1. See above.

#### **11. CONSULTATION UNDERTAKEN**

11.1. Not applicable.

#### **LOCAL GOVERNMENT ACCESS TO INFORMATION ACT 1985**



##### **Background Documents:**

None

**Contact Officer:** Steffan Owen NWRWTP



## Appendix 1 Graphs of results of consultation process thus far

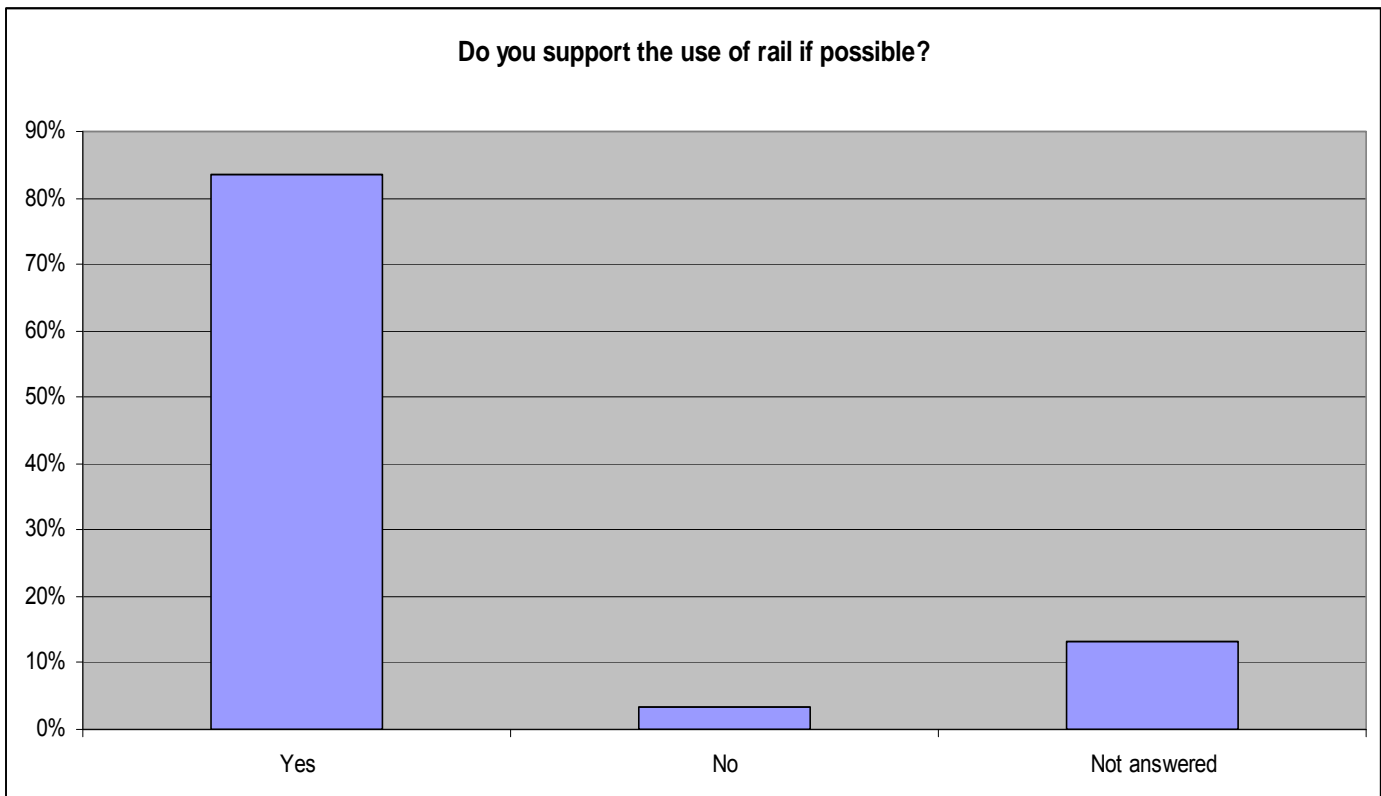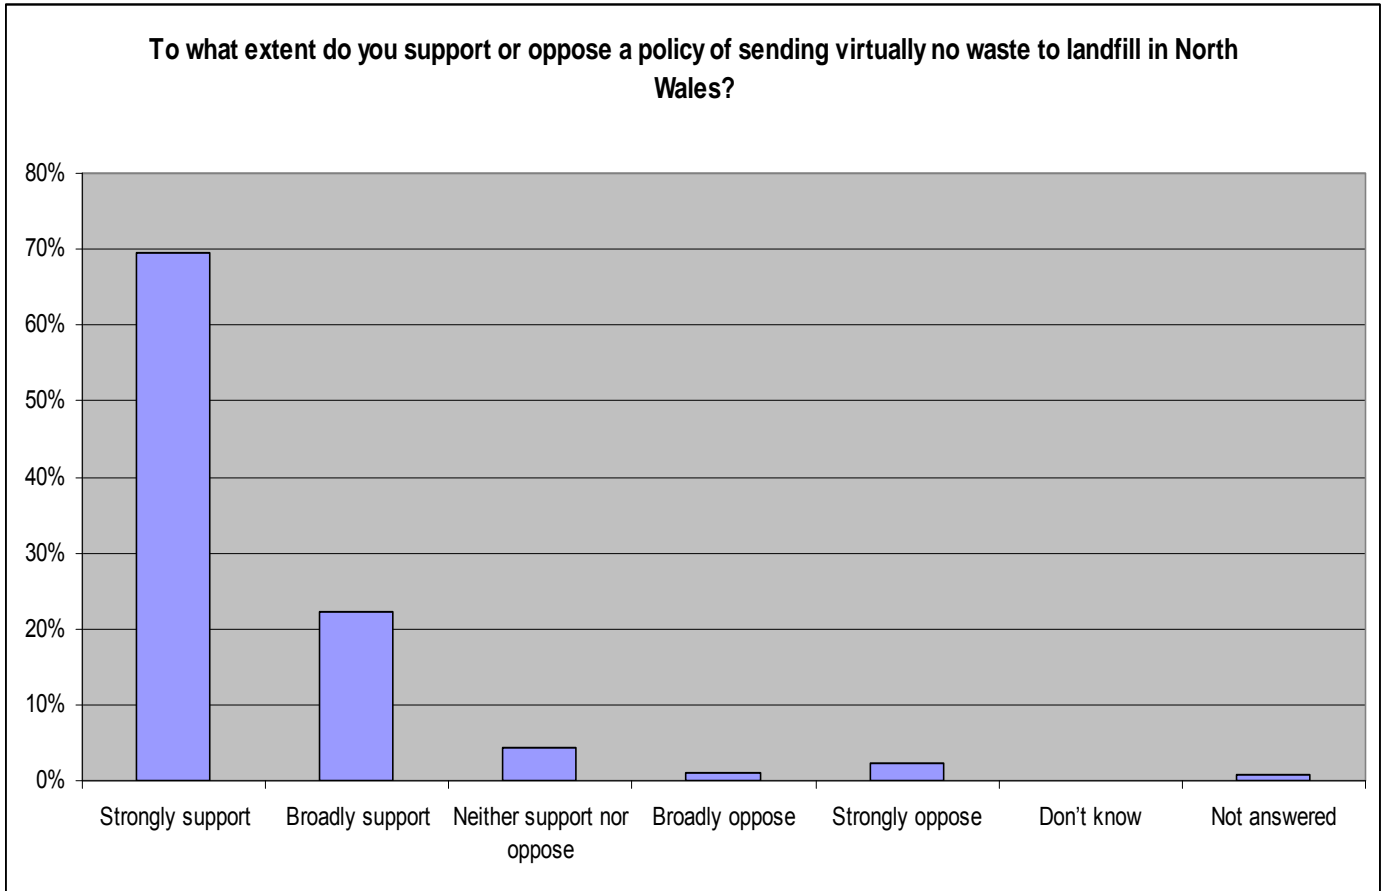





# NWRWTP

North Wales Residual Waste Treatment Project

## To what extent do you support the use of rail is possible?

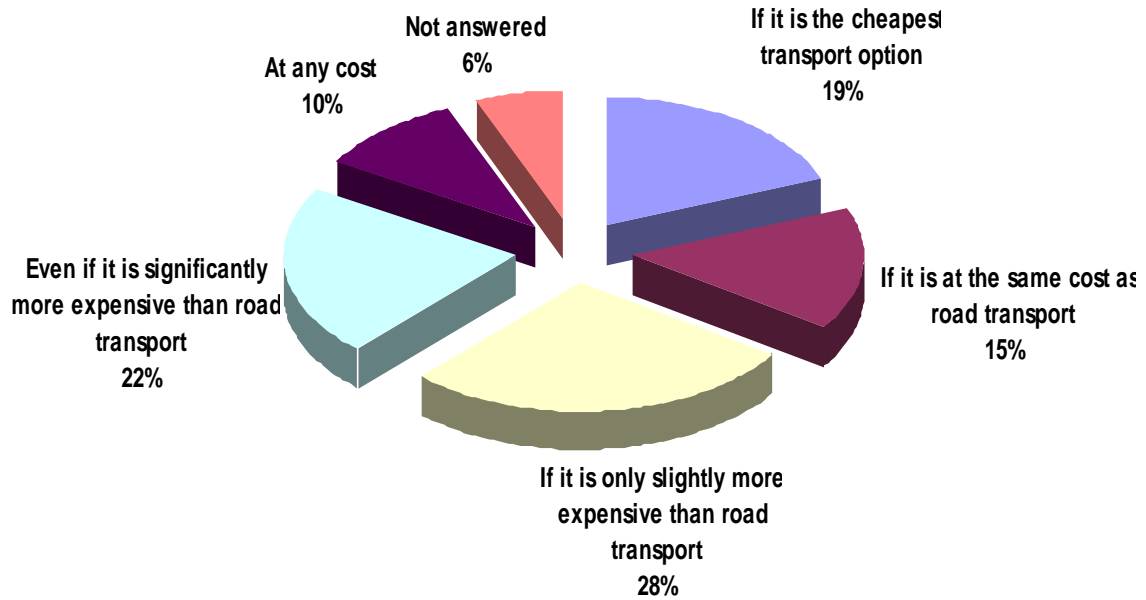

## Where the waste will come from

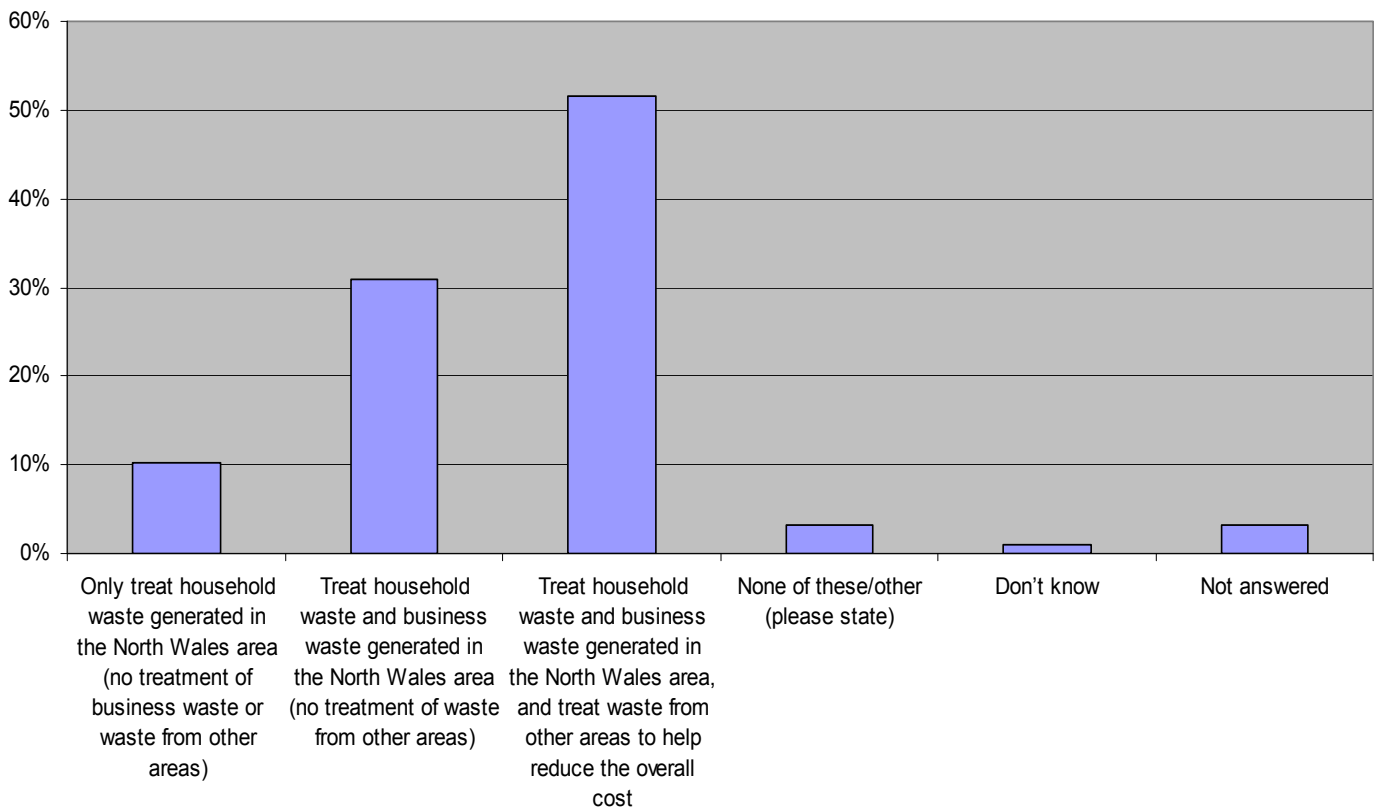



## Appendix 2 – Examples of some of the press coverage

# County residents urged to have say on waste incinerator plans

### RESIDENTS are being urged to have their say on controversial plans which could see an incinerator built on Deeside.

A consultation was launched this week into the Welsh Government's £142.7 million North Wales Residual Waste Treatment Project (NWRWTP) set up to manage waste across five councils in the region.

The prospects of an incinerator on Deeside have been described as a "real threat".

An outline business case presented by project bosses caused anger when it gave Deeside Industrial Estate as the only example of a possible location for an incinerator to handle waste which cannot be recycled.

Now people in Flintshire, Denbighshire, Anglesey,

Gwynedd and Conwy are being asked for their views on the waste treatment facility.

Steffan Owen, project manager for NWRWTP, said: "We have created a leaflet and want to inform people about the project.

"There are questions in the leaflet and the answers given will inform the direction in which we proceed."

Questions include asking people for their views on recycling, on transporting waste by rail and from how far away the new facility should take waste.

Connah's Quay Central councillor Aaron Shotton said the Health Protection Agency was researching the link between infant mortality and incinerator sites in England.

He said: "Given the health effects have not been disproved, I would still urge Flintshire Council to rule out incineration and rule out

Deeside as an option.

"The people of Deeside do not want this and it is important they understand an incinerator on Deeside is a very real threat.

"There is a real and present danger," and Cllr Shotton urged residents to join a campaign against a site in Deeside.

Residents are also asked for their views on benefits the project could bring to the area, such as employment opportunities and the ability to use heat from treating the waste as a power source.

Anxious councillors opposed to an incinerator on Deeside are urging people to fill in the questionnaire.

Connah's Quay councillor Bernie Attridge said: "I'm entirely opposed to an incinerator on Deeside and I will campaign against it.

"I was always told by officers taking this project forward they were energy neutral, but the shortlisted three all specialise in getting energy from waste and that means incinerators. I know a decision has not been made yet but the longer this process goes on the more concerned I am for Deeside."

But project bosses insist Deeside is not confirmed as the definite site. "The document had to name a potential site and potential technology," said Mr Owen. "We put Deeside in because it's

a potential site."

Mr Owen's colleague John Twitchen said: "We couldn't just name a site in make believe, it had to be suitable.

"The land is owned by Flintshire Council and it is also in the development plan for suitable development.

"What might be built and where it might be built is not yet determined."

Mr Owen said bidders are welcome to submit other potential sites in their plans.

The project team has also identified a potential site in Anglesey and is in talks with Anglesey Aluminium to finalise an agreement to list their land as a possible location.

Consultation leaflets are available from today and feedback can also be given at [www.nwrwtp.org](http://www.nwrwtp.org).

Details of drop in sessions for the public, planned for later this summer, are still to be confirmed.

● **WHAT do you think about the project? Have your say at [www.leaderlive.co.uk](http://www.leaderlive.co.uk)**



■ Cllr Bernie Attridge.



■ Cllr Aaron Shotton.





# NWRWTP

North Wales Residual Waste Treatment Project

## Consultation begins on waste site

**PUBLIC** consultation has begun over multi-million pound plans to process non-recyclable waste.

Up to 150,000 tonnes of rubbish from five counties across North Wales could be dumped on Anglesey if the scheme gets the go-ahead.

Land belonging to Anglesey Aluminium Ltd has been earmarked as a possible location for an incinerator.

North Wales' five main councils have joined forces to create the region's largest joint local government

procurement project.

It represents an investment of up to £800m over its 25-year lifetime.

The partnership, called the North Wales Residual Waste Treatment Project (NWRWTP), has invited firms to draw up plans for

processing plants like incinerators to deal with waste currently put into landfill.

As well as Anglesey, a site in Deeside, Flintshire, has been identified prompting some concerns from people living nearby.



Anglesey Aluminium





# NWRWTP

North Wales Residual Waste Treatment Project

BBC News - Deeside waste incinerator consultation begins - Microsoft Internet Explorer provided by Flintshire County Council

http://www.bbc.co.uk/news/uk-wales-north-east-wales-14067745

File Edit View Favorites Tools Help

Wales Politics | North West | **North East** | Mid | South West | South East

9 July 2011 Last updated at 10:05

## Deeside waste incinerator consultation begins

**Public consultation has begun over multi million pound plans to process non-recyclable waste in north Wales.**

Officials have invited firms to draw up plans for processing plants like incinerators to deal with waste currently put into landfill.

So far, two potential sites have been earmarked on Anglesey, Gwynedd, and in Deeside, Flintshire, prompting some concerns from people nearby.

Residents are now being given the opportunity to have their say.

North Wales' five main councils have joined forces to create the region's single largest joint local government procurement project.

The Welsh Government has agreed to put £142m into the project

It represents an investment of up to £800m over its 25-year lifetime.

Flintshire council is taking the lead among the group made up of authorities covering Anglesey, Gwynedd, Conwy, and Denbighshire.

The partnership is called the North Wales Residual Waste Treatment Project (NWRWTP).

Last year, they announced Deeside Industrial Estate could potentially be used as a site to locate an energy from waste incinerator.



**Top Stories**

- BAE confirms loss of 3,000 posts
- Miliband attacks 'fast buck' UK
- Dad's Army co-creator Croft dies **NEW**
- Knox no femme fatale, lawyer says
- Shares up on eurozone rescue hope

**Features & Analysis**

- Headphone generation**  
Has the iPod turned us all into anti-social people?
- Courtroom date**  
Michael Jackson's personal doctor set to face manslaughter charge
- Call centre relocation**  
Do people have a problem with Indian accents?
- Surgical slicing**  
The gloves are off in fight for NHS savings

**Most Popular**

Shared Read Video/Audio

Error on page.

## BBC News Wales Website- 9 July 2011

BBC News - £800m North Wales Residual Waste Treatment talks start - Microsoft Internet Explorer provided by Flintshire County C

http://www.bbc.co.uk/news/uk-wales-north-east-wales-14415802

File Edit View Favorites Tools Help

Wales Politics | North West | **North East** | Mid | South West | South East

5 August 2011 Last updated at 07:52

## £800m North Wales Residual Waste Treatment talks start

**Public consultation is starting over plans to process non-recyclable waste in north Wales, possibly building an incineration plant.**

Two sites in Deeside and Anglesey have been earmarked in the £800m project.

Officials say nothing has been finalised and all ideas are being considered.

They are holding talks with residents across the region, starting at Holyhead on Friday.

North Wales' five main councils have joined forces and invited firms to draw up plans for processing plants [like incinerators to deal with waste currently put into landfill.](#) **2011-09-27 (Press ENTER to Insert)**

They expect it will process more than 150,000 tonnes of waste a year in a project costing an estimated £800m over 25 years.

Flintshire council is taking the lead among the group made up of authorities covering Anglesey, Gwynedd, Conwy, and Denbighshire.


The partnership is called the North Wales Residual Waste Treatment Project (NWRWTP).

**'People against'**

Councillor Eryl Williams, chair of the NWRWTP's joint committee, said the Welsh Government has set target of recycling 70% of household waste by 2025, and using landfill was no longer an option.

He told BBC Radio Wales "there are bound to be people against" plans put forward.

"People don't want things on their doorstep," he said.



The plan is to process 150,000 tonnes of non-recyclable waste a year

**Related Stories**

- Next phase in £800m waste project
- Jobs and tourism 'balance needed'
- Council discusses new waste plan

**Top Stories**

- BAE confirms loss of 3,000 posts
- Miliband attacks 'fast buck' UK
- Dad's Army co-creator Croft dies **NEW**
- Knox no femme fatale, lawyer says
- Shares up on eurozone rescue hope

**Features & Analysis**

- Headphone generation**  
Has the iPod turned us all into anti-social people?
- Courtroom date**  
Michael Jackson's personal doctor set to face manslaughter charge
- Call centre relocation**  
Do people have a problem with Indian accents?
- Surgical slicing**  
The gloves are off in fight for NHS savings

**Most Popular**

Shared Read Video/Audio

Daughter found after three years	1
Comedy creator David Croft dies	2
'Cover up', farmer tells Rihanna	3
MP's wife in kitten theft trial	4

**PUBLIC MEETINGS**

- **ANGLESEY:** Boston Centre Stage, Boston Street, Holyhead; 5 August, 14:00-19:00 BST and 6 August 10:00-16:00 BST

Done

## BBC News Wales Website- 5 August 2011



# NWRWTP

North Wales Residual Waste Treatment Project

## Appendix 3 – attendance at the June 2011 Member sessions, and a list of the questions asked at the sessions.

Friday 17 <sup>th</sup> June 2pm Ty Menai (Formerly Technium CAST) Parc Menai , Bangor	Attended ✓
Cynghorydd RH Wyn Williams (G)	✓
Councillor Gail Hall (C)	✓
Councillor Robert Llewelyn Jones (A)	✓
Councillor Ioan Thomas (G)	✓
Councillor Eurfryn Davies (A)	✓
Councillor Goronwy Parry (A)	✓
Councillor Peter Rogers (A)	✓
Councillor Edward T Dogan	✓
Cynghorydd Eric M Jones (G)	✓
Cynghorydd Gwilym Williams (G)	✓
Councillor Ian Jenkins (C)	✓
Councillor Mike Rayner (C)	✓
Councillor Alwyn Gruffydd (G)	✓
Councillor John Wynn Jones (G)	✓





# NWRWTP

North Wales Residual Waste Treatment Project

<b>Tuesday 28<sup>th</sup> June 9.30am Optic Technium, St. Asaph</b>	<b>Attended ✓</b>
Councillor Carolyn Thomas (F)	✓
Councillor Jim Falshaw (F)	✓
Councillor Brian Cossey (C)	✓
Councillor Nancy Matthews (F)	✓
Councillor Huw Jones (D)	✓
Councillor Christine Jones (C)	✓
Councillor Eng. Klaus Armstrong-Braun (F)	✓
Councillor Christine Evans (D)	✓
Councillor Dave Mackie (F)	✓
Councillor Doreen Mackie (F)	✓
Councillor Susan Shotter (C)	✓
Councillor Dewi Owens (D)	✓
Councillor Eric Owen (F)	✓
Councillor Robin Baker (F)	✓
Councillor Mrs MC Doyle (C)	✓
Councillor William Knightly (C) (poss)	✓
Councillor Mike Priestley (C)	✓
Councillor Chris Bithell (F)	✓
Councillor Ronald Peacock (C)	✓
Councillor John Bevan (C)	✓
Councillor Geoff Corry (C)	✓
Councillor Andrew Hinchliff (C)	✓
Councillor Keith Marshall (G)	✓
Councillor Dennis Hutchinson (F)	✓
Councillor Aaron Shotton (F)	✓
Councillor David Cox (F)	✓
Councillor Raymond Hughes (F)	✓
Councillor Neville Phillips (F)	✓
Councillor Colin Legg (F)	✓
Councillor Gwilym Charles Evans (D)	✓
Councillor Cefyn Henry Williams (D)	✓
Councillor Huw Jones (D)	✓
Councillor Michael John Eckersley (D)	✓
Councillor AM Khan (C) (poss)	✓
Councillor Grenville James (F)	✓
Councillor Bill Cowie (D)	✓
Councillor Ken Stone (D) – Town Council (Mayor of Kinmel Bay & Towyn)	✓



# NWRWTP

North Wales Residual Waste Treatment Project

## Questions Raised

### **17 June 2011**

- What percentage of waste will be sent to recovery?
- Does this solve the landfill problem?
- Is there enough waste for the facility?
- How will the £600 million be allocated across the local authorities, will there be a penalty if we miss the minimum tonnage? Will we have to divert recycling to energy recovery?
- How much energy will it produce and what are the emissions?
- Keep Wales tidy - take it to England! But I do understand, there is economic benefit in doing it here, but why can't we do it ourselves, employ a Welsh company?
- What are the problems with the gateway to the EU, will we see waste imported?
- Corks used to be made out of cork, now they are not which is bad for cork trees. Now we have this waste that we didn't have – what can be done?
- Will it all be taken by rail? e.g. Gwynedd
- Will there be a mobile visitor centre?
- Are we creating something we don't need?

### **28 June 2011**

- From the seven bids received at ISOS, were there any alternatives to energy from waste?
- How can new technologies ever develop if we can't select one and back it?
- Has the timescale slipped?
- I have been bombarded by information from Friends of the Earth, are their claims correct?
- How sound is the technology and how tried and tested is it?
- Why not Mechanical Biological Treatment (MBT)?
- Will there be compensation if you don't fill the facility?
- Germany re-uses residual waste from energy from waste – will we?
- What happens if there is not enough waste?



# NWRWTP

North Wales Residual Waste Treatment Project

- What about legislation affecting commercial waste collectors, is it the same/are there targets?
- Public need to be convinced that we need this, they need information – what's being done?
- It's not really technology neutral, we were supposed to be technology neutral, are councillors finding out about this change in position when it's already too late?
- Where are the sites?
- Will it be transboundary? Will commercial waste come from outside Wales?
- What about Wrexham, will they be involved in this?
- Will people be happy to accept the facility near them?

FLINTSHIRE COUNTY COUNCIL

EXEMPT INFORMATION SHEET

---

COMMITTEE: NWRWTP Joint Committee

DATE: 6 October, 2011

AGENDA ITEM NO: 8

REPORT OF: Project Director

---

SUBJECT: Waste Flow Model Update

---

The Report on this item is NOT FOR PUBLICATION because of exempt information in accordance with the following section(s) or paragraph(s) of Schedule 12A of the Local Government Act 1972:

	<u>Para</u>	
Information relating to a particular individual *	12	[ ]
Information likely to reveal the identity of an individual *	13	[ ]
Information relating to financial/business affairs of a particular person * See Note 1	14	[✓]
Information relating to consultations/negotiations on labour relations matter *	15	[ ]
Legal professional privilege	16	[ ]
Information revealing the authority proposes to:		
(a) give a statutory notice or		
(b) make a statutory order/direction *	17	[ ]
Information on prevention/investigation/prosecution of crime *	18	[ ]
<u>For Standards Committee meetings only:</u>	<u>Sec</u>	
Information subject to obligations of confidentiality	18A	[ ]
Information relating to national security	18B	[ ]
The deliberations of a Standards Committee in reaching a finding	18C	[ ]
Confidential information which the Council is not permitted to disclose	100A	[ ]
	(3)	

**PLEASE TICK APPROPRIATE BOX**

\* Means exempt only if the public interest in maintaining the exemption outweighs the public interest in disclosing the information.

Note 1: Information is not exempt under paragraph 14 if such information is required to be registered under Companies Act 1985, the Friendly Societies Acts of 1974 and 1992, the Industrial and Provident Societies Act 1965 to 1978, the Building Societies Act 1986 or the Charities Act 1993.

**SCHEDULE 12A LOCAL GOVERNMENT ACT 1972  
EXEMPTION FROM DISCLOSURE OF DOCUMENTS**

**REPORT:** Waste Flow Model Update

**AUTHOR:** Project Director

**MEETING AND DATE OF MEETING:** NWRWTP Joint Committee  
6 October, 2011

I have considered grounds for exemption of information contained in the report referred to above and make the following recommendation to the Proper Officer:-

**Exemptions applying to the report:**

Paragraph 14

**Factors in favour of disclosure:**

Transparency

**Prejudice which would result if the information were disclosed:**

The report contains information which if disclosed at the present time could prejudice a fair bidding process.

**My view on the public interest test is as follows:**

On balance, at the present time it is not in the public interest to make the information publicly available.

**Recommended decision on exemption from disclosure:**

Exempt from disclosure

**Date:** 28 September, 2011

**Signed:**



**Post:** Team Manager – Committee Services

---

I accept the recommendation made above.



---

Proper Officer

Date: 28 September, 2011



**Barry Davies LL.B (Hons)**  
**Solicitor/Cyfreithiwr**  
 Head of Legal and Democratic Services  
 Pennaeth Gwasanaethau Cyfreithiol a  
 Democraidaidd

I: Cyngorwyr: Nancy Matthews, N. Phillips, Michael Priestly,  
 Eryl Williams, Arwel Pierce, W. G. Roberts, Sharon Frobisher,  
 Meirion Hughes a Alex Aldridge

CS/NG

28 Medi, 2011

Nicola Gittins

01352 702345

[nicola.gittins@flintshire.gov.uk](mailto:nicola.gittins@flintshire.gov.uk)

Annwyl Syr / Fadam

Cynhelir **CYFARFOD CYD-BWYLLGOR GWASTRAFF GWEIDDILLIOL GOGLEDD CYMRU yn SIAMBR ARFON, SWYDDFA ARDAL ARFON, PENRALLT, CAERNARFON, GWYNEDD, LL55 1BN ar DYDD IAU, 6 HYDREF, 2011 am 10.30y.b.** i drafod y materion canlynol.

Yr eiddoch yn gywir

Rheolwr Democratiaeth a Rheolaeth

## **A G E N D A**

1. **YMDDIHEURIADAU**
2. **DATGAN DIDDORDEB**
3. **CYMERADWYO COFNODION BLAENOROL**
4. **MATERION YN CODI O'R CYFARFOD BLAENOROL**

County Hall, Mold. CH7 6NA  
 Tel. 01352 702400 DX 708591 Mold 4  
[www.flintshire.gov.uk](http://www.flintshire.gov.uk)  
 Neuadd y Sir, Yr Wyddgrug. CH7 6NR  
 Ffôn 01352 702400 DX 708591 Mold 4  
[www.siryfflint.gov.uk](http://www.siryfflint.gov.uk)

The Council welcomes correspondence in Welsh or English  
 Mae'r Cyngor yn croesawau gohebiaeth yn y Cymraeg neu'r Saesneg

5. **ADRODDIAD CYNYDD (ADRODDIAD SO)**
6. **RIR – DIWEDDARIAD STATWS RISG (ADRODDIAD SP)**
7. **DIWEDDARIAD CYFATHREBU (ADRODDIAD SO)**

**DEDDF LLYWODRAETH LEOL (MYNEDIAD AT WYBODAETH) 1985 – I  
GYSIDRO EITHRIO'R WASG A'R CYHOEDD**

Mae'r eitem isod yn cael ei gysidro fel eitem i'w eithrio dan paragraff(au) 1 o Rhan 1 o Atodlen 12A o Ddeddf Llywodraeth Lleol 1972 (fel a ddiwygwyd)

8. **ADRODDIAD MODEL LLIF GWASTRAFF (ADRODDIAD SP)**
9. **UNRHYW FATER ARALL**



**PTGGGC**

Prosiect Trin Gwastraff Gweddilliol Gogledd Cymru

## **CYD BWYLLGOR GWASTRAFF GWEDDILLIOL GOGLEDD CYMRU**

Cofnodion cyfarfod y Cyd Bwyllgor a gynhaliwyd yn Siambr y Cyngor, Bodlondeb, Conwy ar ddydd Gwener, 3 Mehefin 2011 am 10.30 am

### **PRESENNOL**

Cynghorydd Eryl Williams – Cyngor Sir Ddinbych (**Cadeirydd**)  
Cynghorydd Mike Priestley – Cyngor Bwrdeistref Sirol Conwy  
Cynghorydd Meirion Hughes – Cyngor Bwrdeistref Sirol Conwy  
Cynghorydd Arwel Pierce – Cyngor Gwynedd  
Cynghorydd Sharon Frobisher – Cyngor Sir Ddinbych  
Cynghorydd Neville Phillips – Cyngor Sir y Fflint  
Alex Aldridge – Comisiynydd Cyngor Sir Ynys Môn

### **HEFYD YN BRESENNOL**

#### **Cyngor Bwrdeistref Sirol Conwy**

Andrew Kirkham (Cyfarwyddwr Corfforaethol Gweithredol a Phennaeth Gwasanaethau Cyllid)

#### **Cyngor Sir Ddinbych**

Steve Parker (Pennaeth Amgylchedd)

#### **Cyngor Gwynedd**

Dilwyn Williams (Cyfarwyddwr Corfforaethol)

#### **Cyngor Sir y Fflint**

Colin Everett (Prif Weithredwr)  
Kerry Feather (Pennaeth Cyllid)  
Louise Pedreschi (Cyfreithwraig)

#### **Cyngor Sir Ynys Môn**

Arthur Owen (Cyfarwyddwr Corfforaethol)  
Meirion Edwards (Prif Swyddog Rheoli Gwastraff)

#### **Prosiect Triniaeth Gwastraff Gweddilliol Gogledd Cymru**

Stephen Penny (Cyfarwyddwr y Prosiect)  
Steffan Owen (Rheolwr y Prosiect)

### **11. YMDDIHEURIADAU**

Derbyniwyd ymddiheuriadau am absenoldeb oddi wrth y Cynghorydd Nancy Matthews (Cyngor Sir y Fflint) a Barry Davies (Pennaeth Gwasanaethau Cyfreithiol a Democrataidd (Cyngor Sir y Fflint))

### **12. COFNODION**

Cyflwynwyd cofnodion cyfarfod y Cyd Bwyllgor Gwastraff Gweddilliol Gogledd Cymru a gynhaliwyd ar 25 Mawrth 2011 i'w cymeradwyo. Nododd Alex Aldridge ei fod yn bresennol yn rhinwedd ei swydd fel Comisiynydd i Gyngor Sir Ynys Môn ac nid fel Cynghorydd Sir i





**PTGGGC**

Prosiect Trin Gwastraff Gweddilliol Gogledd Cymru

Gyngor Sir y Fflint. Dywedodd Mr Aldridge na ddylid cyfeirio ato fel Cynghorydd mewn unrhyw gofnodion i'r dyfodol.

Ymhellach, roedd Mr Aldridge wedi datgan diddordeb yn y cyfarfod diwethaf gan ei fod hefyd yn Gyngorydd Sir i Gyngor Sir y Fflint, Awdurdod Lleol partner i'r PTGGGC.

#### **PENDERFYNWYD-**

**Yn destun i'r diwygiadau uchod, bod cofnodion cyfarfod y Cyd Bwyllgor Gwastraff Gweddilliol Gogledd Cymru a gynhaliwyd ar 25 Mawrth 2011 gael eu cymeradwyo fel cofnod cywir.**

#### **13. DATGAN DIDDORDEB**

Datganodd Alex Aldridge, Comisiynydd i Gyngor Sir Ynys Môn, ddiddordeb personol gan ei fod hefyd yn Cynghorydd Sir i Gyngor Sir y Fflint.

#### **14. ADRODDIAD CYNNYDD**

Cyflwynodd y Rheolwr Prosiect adroddiad cynnydd a nododd fod y prosiect yn symud ymlaen o fewn ei gyllideb a bod y gwariant terfynol ar gyfer 2010/11 yn £867,431.71 a oedd yn cyfateb i £173,486.43 fesul Awdurdod Lleol.

Nid oedd unrhyw broblemau mawr a rhoddodd ddiweddariad ynghylch mân faterion yng ngweithgaredd y prosiect fel a ganlyn:-

- ID 32 – Penawdau'r telerau (HoTs) wedi'u llofnodi. Yn dilyn pryderon gan yr Awdurdod Priffyrdd priodol ynghylch y safle arfaethedig yn Alwminiwm Môn roedd trafodaethau yn mynd yn eu blaen i ddatrys y materion hynny. Cafwyd cyfarfod gyda'r perchennog tir a gobeithid y byddai'r holl faterion wedi eu datrys erbyn Mehefin 2011
- ID 42 – Cafwyd cyfarfodydd gyda Llywodraeth Cymru (LIC) yng nghyswllt ffrwd ariannu bosib ar gyfer prosiectau cysylltiedig â'r rheilffordd. Byddai adborth gan Aelodau ar brosiectau rheilffordd posib yn cael eu darparu i weithdai PTGGGC i'r dyfodol
- ID 59 – Heblaw am y Cytundeb Prosiect roedd yr holl ddogfennaeth Gwahoddiadau i Gyfranogi mewn Deialog (ITCD) wedi eu hanfon
- ID 60 – Cafwyd saith sesiwn gyda chyfranogwyr i drafod safleoedd trosglwyddo gwastraff a gweithgareddau cysylltiedig â gwastraff. Byddai angen cwblhau'r holl faterion technegol cyn y gallai'r prosiect symud ymlaen i drafod y materion masnachol
- ID 61 – Roedd ffigyrau diweddaraf llif gwastraff wedi eu cyhoeddi a byddai'r model llif gwastraff yn cael ei seilio ar y ffigyrau diweddaraf hynny. Byddai adroddiad ar y ffigyrau llif gwastraff hynny'n cael ei gyflwyno yng nghyfarfod nesaf y



# PTGGGC

Prosiect Trin Gwastraff Gweddilliol Gogledd Cymru

PTGGGC.

Yng nghyswllt y fenter ddiweddaraf gan Lywodraeth San Steffan i gysidro ddarparu arian i Gynghorau ar gyfer casglu biniau'n wythnosol, ni fyddai hyn yn effeithio ar Gymru. Roedd gan LIC ei phwerau ei hun i ddelio â chasglu gwastraff ac roedd wedi rhoi arwydd clir y byddai Cymru'n parhau â chasgliad bob pythefnos. Petai casglu biniau'n wythnosol yn cael ei roi ymlaen gan LIC, byddai angen meddwl am ddatrysiadau fel lleihau cynhwysedd biniau.

- ID 70 – Adroddiad ar Brosiectau Ffyrdd/Rheilffyrdd yn cael ei gyflwyno yng nghyfarfod o'r PTGGGC yn y dyfodol.
- ID 71 – Byddai'n bosib y bydd arwydd cynnar o bris y datrysiadau trin gwastraff ar gael yn Awst 2011
- ID 78 – Byddai'r ail Gytundeb Rhyng Awdurdod (IAA) yn cychwyn unwaith yr oedd y datrysiadau trin gwastraff yn hysbys

#### **PENDERFYNWYD-**

**Nodi'r adroddiad cynnydd ar gyfer y prosiect.**

#### **15. RIR – DIWEDDARIAD STATWS RISG**

Cyflwynodd y Cyfarwyddwr y Prosiect yr Adroddiad Cofrestr Risg, a oedd yn amlygu rhai o'r diwygiadau a wnaethpwyd i adlewyrchu'r ddealltwriaeth bresennol o risg a'r mesurau lliniaru sydd yn eu lle.

Dynodwyd risg yng nghyswllt ymgynghoriad LIC ar y cynlluniau sector newydd ar gyfer Cynllun Sector Casgliadau, Seilwaith, a Marchnad, a Chynllun Sector Bwyd, Gwasanaethau a Manwerthu. O fewn yr ymgynghoriadau, cyfeirir at gyflwyniad posib treth ar wastraff i ynni, er bod y dogfennau'n cydnabod nad oes gan LIC presennol y pŵer i wneud hyn. Yn dilyn ymateb gan LIC cydnabuwyd fod nad oedd y cyfeiriad hwn at dreth ar ynni gwastraff yn bolisi ffurfiol ac y byddai'n debygol o gael ei ddileu o'r Cynlluniau. Fodd bynnag, hyd nes y bo'r Cynlluniau Sector terfynol yn cael eu cyhoeddi, byddai'n parhau'n risg.

Nid oedd gan Aelodau unrhyw faterion i godi yng nghyswllt y risgiau a amlinellwyd yn atodiad 1, na'r newidiadau a wnaethpwyd yn y cyfnod fel yr amlinellwyd yn atodiad 2.

#### **PENDERFYNWYD-**

**Nodi'r gofrestr risg wedi'i diweddarau ar gyfer y prosiect.**

#### **16. DIWEDDARIAD CYFATHREBU**

Rhoddodd Rheolwr y Prosiect ddiweddariad i Aelodau yng nghyswllt materion Cyfathrebu PTGGGC.

Cyhoeddwyd datganiad i'r wasg yn cyhoeddi fod y prosiect mewn trafodaethau ag Alwminiwm Môn ynghylch sicrhau rhan o'r safle i'r



# PTGGGC

Prosiect Trin Gwastraff Gweddilliol Gogledd Cymru

prosiect. Hefyd cyhoeddwyd Newyddlen Aelodau gyda'r un wybodaeth.

Cyflwynwyd llyfryn ymgynghori drafft i Aelodau am sylwadau. Unwaith y bydd wedi ei orffen, bydd y llyfryn yn cael ei argraffu a'i gylchu i leoliadau perthnasol fel Swyddfeydd Cyngor, llyfrgelloedd, canolfannau hamdden ayb.

Byddai Sesiynau Aelodau'n cael eu cynnal ar Ddydd Gwener, 17 Mehefin 2011 am 2.00 pm ym Mangor a Dydd Mercher 29 Mehefin 2011 am 2.00 pm yn Llanelwy. Gan mai dim ond llond dwrn o Aelodau oedd wedi cadarnhau eu presenoldeb yn y sesiynau, awgrymwyd anfon nodyn atgoffa gwahoddiad cyn gynted â phosib.

Roedd sylwadau ac atebion i ymholiadau Aelodau fel a ganlyn:-

- Eisoes cafwyd adborth cwsmeriaid, fodd bynnag byddai'r ymgynghoriad yn rhoi'r dystiolaeth sydd ei hangen i gefnogi unrhyw Geisiadau Cynllunio sy'n ymwneud â'r Prosiect. Ymhellach, byddai sawl opsiwn yn cael ei gynnig i'r Prosiect a gallai'r ymgynghoriad ddylanwadu ar y datrysiad
- Byddai'r Sesiynau gweithdy'n cael eu hwyluso gan Reolwr y Prosiect, Cyfarwyddwr y Prosiect a John Twitchen o Sauce Consultancy
- Yng nghyswllt ymgynghori, awgrymwyd yr opsiynau canlynol:-
  - Sesiynau Galw Heibio
  - Sioeau ffordd mewn Archfarchnadoedd a Chanolfannau Siopa
  - Arolygon Ffôn
  - Gweithlu trwy ryngrwyd i bartneriaid perthnasol
  - Gweithlu Sefydliadau Partner fel Parc Cenedlaethol Eryri, Gwasanaeth Tân ac Achub Gogledd Cymru, Heddlu Gogledd Cymru, a Bwrdd Iechyd Prifysgol Betsi Cadwaladr trwy eu gwefannau

Yng nghyswllt pryderon am Aelodau'n cyn-benderfynu Cais Cynllunio drwy eu rôl fel Aelod Etholedig, dylid rhoi cyngor priodol i Aelodau yn y gweithdai. Ymhellach, dylid anfon llythyr gyda'r ymgynghoriad i Aelodau. Dylid atgoffa Aelodau os ydynt yn defnyddio'u rôl fel Aelod Adran Etholiadol leol i leisio eu pryderon yn gyhoeddus, byddai hyn yn cael ei ystyried fel cyn-benderfyniad ac felly buasent yn cael eu gwahardd o unrhyw benderfyniad pwyllgor Cynllunio.

## **PENDERFYNWYD-**

- (a) Nodi cylchu'r Datganiad i'r Wasg a Newyddlen Aelodau.**
- (b) Cymeradwyo'r llyfryn ymgynghoriad.**
- (c) Anfon gwahoddiad i atgoffa Aelodau am y Sesiynau Gweithdy.**
- (d) Anfon llythyr at yr holl Aelodau, gyda'r llyfryn**



**PTGGGC**

Prosiect Trin Gwastraff Gweddilliol Gogledd Cymru

## **ymgyngoriad, yn rhoi cyngor iddynt o'u gweithredoedd yng nghyswllt cyn-benderfynu.**

### **17. DIWEDDARIAD CAFFAEL RHEILFFYRDD**

Diweddarodd y Cyfarwyddwr y Prosiect yr Aelodau ar y dull arfaethedig o ystyried mabwysiadu posib rheilffyrdd fel rhan o'r datrysiad PTGGGC yn y broses gaffael.

Mae'r Bartneriaeth wedi ei gwneud yn glir i Gyfranogwyr, drwy gydol y broses gaffael hyd yma, fod y Bartneriaeth eisiau archwilio defnydd posib rheilffyrdd fel rhan o unrhyw ddatrysiad y gellir ei ddatblygu ar gyfer y Prosiect.

Yn dilyn trafodaeth yn y tîm prosiect, a'i gynghorwyr cyfreithiol allanol, argymhellwyd proses sy'n rhoi risg isel o herio, ac sy'n dal i alluogi'r Bartneriaeth i wneud penderfyniad polisi ar p'un a yw'n dymuno datrysiad seiliedig ar ffyrdd neu reilffyrdd ar y cam priodol.

Yn fyr y broses oedd:-

- Y cam Gwahoddiad i Gyflwyno Atebion Manwl (ISDS) yn ei gwneud yn ofynnol i Gyfranogwyr gyflwyno datrysiadau ffyrdd a rheilffyrdd wedi'u datblygu'n llawn ym Medi 2011
- Partneriaeth i asesu'r cyflwyniadau a phenderfynu ar ddatrysiad ffyrdd neu reilffyrdd yng nghyfarfod y Cydbwyllgor PTGGGC a gynhelir yn Hydref 2011. Ni fyddai unrhyw gyfranogydd yn cael ei ddad-ddethol ar y cam hwn
- Hysbysu Cyfranogwyr o benderfyniad y Bartneriaeth (datrysiad seiliedig ar ffyrdd neu reilffyrdd) a rhoi 3 wythnos arall iddynt fireinio eu datrysiad (trwy Wahoddiad i Gyflwyno datrysiadau wedi'u mireinio - ISRF)
- Ymatebion ISRF y cyfranogwyr yn cael eu cyflwyno yn Nhachwedd 2011 gyda'r Bartneriaeth yn gwneud ei benderfyniad ar y ddau Gyfranogydd i fynd drwodd i'r cam CFT yn Ionawr 2012
- Mae'r broses dau gam yn ymestyn y broses gaffael gan hyd at 3 mis, ond barn y tîm prosiect oedd bod angen y cam ychwanegol hwn i sicrhau y gellir ystyried y rheilffordd yn briodol

Roedd y Cyfarwyddwr y Prosiect yn hyderus yn dilyn asesiad cychwynnol ynghylch mynediad rhwydwaith y byddai'r Cyfranogwyr yn medru cyflenwi cyflwyniad rheilffordd. Cynghorwyd Aelodau ymhellach fod gan Alwminiwm Môn derfynfa rheilffordd wedi'i leoli ar y safle.

### **PENDERFYNWYD-**

**Cymeradwyo'r dull caffael arfaethedig er mwyn galluogi'r Bartneriaeth i benderfynu ei bolisi dewisol yng nghyswllt defnyddio'r ffyrdd neu'r rheilffyrdd fel y sail ar gyfer y**



**PTGGGC**

Prosiect Trin Gwastraff Gweddilliol Gogledd Cymru

## **datrysiadau**

### **18. UNRHYW FATER ARALL**

Cynghorwyd Aelodau fod Cyfeillion y Ddaear wedi cyhoeddi datganiad briffio. Roedd ymateb i'r datganiad hwnnw wedi ei anfon at ENTEC am ei fewnbwn technegol. Byddai'r ymateb yn cael ei anfon at Aelodau am sylwadau ond rodd angen ateb erbyn Dydd Llun, 6 Mehefin 2011 er mwyn galluogi'r ymateb i gael ei anfon erbyn prynhawn y diwrnod hwnnw.

**EITEM AGENDA RHIF 5****ADRODDIAD CYNNYDD CYDBWYLLGOR GWASTRAFF GWEDDILLIOL GOGLEDD CYMRU****CYDBWYLLGOR GWASTRAFF GWEDDILLIOL GOGLEDD CYMRU****Dyddiad: 6 Hydref 2011****Cyfnod: 26 Mai 2011 i 28 Medi 2011****CRYNODEB Y PROSIECT**

I gaffael datrysiad rheoli gwastraff cynaliadwy i'r 5 awdurdod lleol yng Ngogledd Cymru (Conwy, Sir Ddinbych, Sir y Fflint, Gwynedd ac Ynys Môn) a fydd yn cynorthwyo â lleihau allyriadau nwyon tŷ gwydr o dirlenwi ac yn lleihau'r tunelledd o weddillion gwastraff a anfonir i dirlenwi a thrwy hynny sicrhau fod yr awdurdodau'n osgoi'r cosbau tordyletswydd Cynllun Lwfans Tirlenwi (LAS) a chwrdd â thargedau'r Strategaeth Wastraff Genedlaethol.

**STATWS Y PROSIECT**

<b>Statws Cyffredinol y Prosiect</b>	
<b>Ambr</b>	Mae deialog wedi bod yn parhau gyda'r tri ymgeiswyr ar faterion cyfreithiol, ariannol a thechnegol. Mae'r broses ymgynghori wedi bwrw ymlaen gyda nifer o seynau wedi'w gynnal ar hyd ardal y Bartneriaeth er mwyn i hapddalwyr a'r cyhoedd gael cyfle i drafod y prosiect.  Un o'r ymgeiswyr wedi gofyn am estyniad i'r amserlen.

<b>Statws Cyllideb</b>	
<b>Gwyrdd</b>	Gwariant y flwyddyn ariannoll hon hyd at 19/08/11 yw £312,096.  Gwariant y flwyddyn ariannoll hon wedi'w brofflio hyd at 31/07/11 yw £405,087 (dan broffil o £92,991).

<b>Statws</b>	<b>Ystyr</b>
<b>Gwyrdd</b>	Nid oes unrhyw broblemau; popeth yn mynd ymlaen yn



	<b>dda ac i'r cynllun</b>
<b>Ambr</b>	Mae rhai problemau bach / llai. Mae angen gweithredu mewn rhai meysydd ond mae rhannau eraill yn bwrw ymlaen yn foddhaol
<b>Coch</b>	Mae problemau sylweddol a rhai brys ac mae angen gweithredu pendant.

**DIWEDDARIAD PROSIECT** – Gweithgareddau sydd i'w cwblhau o 7<sup>fed</sup> Ionawr 2011 i 18<sup>fed</sup> Mawrth 2011 (a gweithredoedd tymor hirach sydd wedi'u lliwoleuo).

ID	Gweithgaredd	Statws RAG	Sylwadau	Rhagolwg	Gwirioneddol
32	Opsiwn wedi'i ddatblygu ar ail safle sydd â'r gallu i'w dderbyn gan y Cyd Bwyllgor	Ambr	Diweddariad ar lafar gan Gyfarwyddwr y Prosiect	Mai 2011	
60	Dynodi materion â defnydd posib o safleoedd presennol sy'n codi o gyflwyniadau ISOS	Gwyrdd	Deialog eang wedi ei gynnal gyda'r ymgwiswyr i gyd. Cytundeb gyffredinol wedi'w gyrraedd gyda bob ymgeisiwr.	Medi 2011	Wedi cwblhau
61	Cysylltu â swyddogion technegol ar lifoedd gwastraff yn dilyn data alldro 2010/11.	Gwyrdd	Sesiynau unigol gyda Amec a'r awdurdodau i fynd trwy'r model llif gwastraff yn fanwl. Sesiynau grwp technegol wedi'i gynnal i gytuno'r rhagolwg llif gwastraff. Gweler eitem 8 ar yr agenda.	Mehefin 2011	Wedi cwblhau
62	Caffael ymgynghorwyr i gynllunio a chynnal ymarfer ymgynghori ar ddull y bartneriaeth	Ambr	Proses ymgynghori wedi cychwyn ym Mis Mehefin 2011.	Diwedd Chwef 2011	Wedi cwblhau
63	Penderfynu ar gefnogaeth ymgysylltu a hwyluso	Ambr	Cefnogaeth hwyluso i'w ddefnyddio yn ôl yr angen. Sauce Consultancy i'w	Mawrth 2011	Wedi cwblhau



# PTGGGC

Prosiect Trin Gwastraff Gweddilliol Gogledd Cymru

			ddefnyddio ar gyfer cymorth a chyngor strategol arbennigol.		
64	Sesiynau deialog Mehefin	Gwyrdd	Cyfarfodydd gyda chyfranogwyr fel rhan o'r broses deialog gystadleuol	Mehefin 2011	Wedi cwblhau
65	Sesiynau deialog Gorffennaf	Gwyrdd	Cyfarfodydd gyda chyfranogwyr fel rhan o'r broses deialog gystadleuol	Gorffennaf 2011	Wedi cwblhau
66	Sesiynau deialog Awst	Gwyrdd	Cyfarfodydd gyda chyfranogwyr fel rhan o'r broses deialog gystadleuol	Awst 2011	Wedi cwblhau
67	Sesiynau deialog Medi	Gwyrdd	Cyfarfodydd gyda chyfranogwyr fel rhan o'r broses deialog gystadleuol	Medi 2011	Wedi cwblhau
68	Pecyn briffio wedi'i roi i swyddogion cynllunio mwynau a gwastraff	Gwyrdd	Pecyn briffio wedi'i wddarparu i Swyddogion.	Mehefin 2011	Wedi cwblhau
69	Rhoi'r Model Llif Gwastraff ISDS i gyfranogwyr	Gwyrdd	Yn dilyn gweithred 61	Diwedd Mehefin 2011	Wedi cwblhau
70	Proses ar gyfer asesu datrysiadau ffordd / ffordd-rheilffordd i'w penderfynu	Gwyrdd	Proses ar gyfer asesu datrysiadau ffordd / ffordd-rheilffordd wedi ei gytuno.	Gorffennaf 2011	Wedi cwblhau
71	Tîm Prosiect i dderbyn arwyddion cynnar o gynnwys cyflwyniadau ISDS posib gan gynnwys gwybodaeth prisio ayyb	Gwyrdd	I roi cymorth i'r Tîm Prosiect mewnol a'r Swyddogion Cyllid awdurdod partner fel nad oes unrhyw "syndod" pan fydd cyflwyniadau ISDS yn cael eu derbyn yn y pen draw.	Awst 2011	Wedi cwblhau
72	Datrysiadau ISDS i'w cyflwyno gan gyfranogwyr	Ambr	Diweddariad ar lafar gan y Gyfarwyddwr Prosiect yn y cyfarfod (gweler atodiad 1 isod am	Diwedd Ionawr 2012	





# PTGGGC

Prosiect Trin Gwastraff Gweddilliol Gogledd Cymru

			amserlen caffael diwygiedig)		
73	Aseiad o gyflwyniadau ISDS	Ambr	Prif wybodaeth wedi'i darparu i Swyddogion Cyllid, Technegol a Chyfreithiol cyn datblygu argymhellion i'r Bwrdd Prosiect a'r Cyd Bwyllgor	Chwefror 2012	
74	Cyfranogwyr yn cael gwybod am benderfyniadau'r bartneriaeth am ffordd / ffordd-rheilffordd, a'u gwahodd i gyflwyno mireiniadau i'w cyflwyniadau ISDS o ystyried y penderfyniad	Ambr	Yn ôl yr amserlen gaffael ddiwygiedig (gweler atodiad 1)	Gynar yn Mawrth 2012	
75	Cyflwyniad o ISDS wedi'i Fireinio gan gyfranogwyr	Ambr	Yn ôl yr amserlen gaffael ddiwygiedig (gweler atodiad 1)	Ebrill / Mai 2012	
76	Gwerthuso cyflwyniadau ISDS wedi'i Fireinio	Ambr	Yn ôl yr amserlen gaffael ddiwygiedig (gweler atodiad 1)	Mai / Mehefin 2012	
77	Safleoedd negodi i'w cytuno gan y Bwrdd Prosiect	Gwyrdd	Bydd y PD yn datblygu nifer o safleoedd "gorau" a "stop cefn" ar gyfer cymeradwyaeth gan y Bwrdd Prosiect, fydd yn cael eu defnyddio i gymryd safleoedd masnachol yn y broses gaffael	Gorffennaf 2011	Wedi cwblhau
78	Yr ail IAA (IAA2) i'w ddechrau	Gwyrdd	Hyn i ddechrau unwaith y bydd datrysiadau ISDS yn wybyddus (a'r strwythurau contract tebygol yn fwy pendant). Rhai	Tachwedd 2011	



# PTGGGC

Prosiect Trin Gwastraff Gweddillio Gogledd Cymru

			trafodaethau rhagarweiniol a gwaith datblygiad i'w gynnal yn ystod haf 2011.		
79	Gwybodaeth teitlau safleoedd partneriaeth a chyfyngiadau cysylltiedig yn cael eu casglu a'u dynodi	Gwyrdd		Mehefin 2011	Wedi cwblhau
80	Tim Prosiect a swyddog cyfreithiol arweiniol i gwedd a'r adran ystadau i drafod unrhyw anghysondebau yn y gwybodaeth teitlau	Gwyrdd		4 Hydref 2011	
81	Amser ychwanegol wedi'i roi ar gyfer ymatebion ymgynghorol	Gwyrdd	Pythefnos wedi ei ychwanegi er mwyn medru cynnwys mor gymaint o ymatebion ag y bo modd	7 Hydref 2011	
82	Dadansoddiad llawn o'r ymatebion ymgynghorol	Gwyrdd	Adroddiad i'w greu yn dangos canlyniadau'r ymarfer ymgynghori	Hydref 2011	
83	Adrodd yn ôl i'r cyhoedd ac atebwyr gyda canlyniadau'r ymgynghoriad	Gwyrdd	I'w gadarnhau (gweler eitem 84 isod)	I'w gadarnhau	
84	Cynllun ar gyfer ymgysylltu a chyfathrebu am y 12 mis nesaf	Gwyrdd	Cyfarfod wedi'w drefnu gyda'r Tim Prosiect, Amec a Sauce Consultancy i gynllunio ymgysylltu a chyfathrebu am y 12 mis nesaf	21 Hydref 2011	
85	Cwrdd a	Gwyrdd		Tachwedd	



# PTGGGC

Prosiect Trin Gwastraff Gweddilliol Gogledd Cymru

	Asiantaeth Amgylchedd Cymru i drafod materion technegol yn codi o'r cynnigion			2011	
86	Deialog pellach cyn cynnigion ISDS	Gwyrdd		Rhagfyr 2011	
87	Timau ariannol a thechnegol i'r ymgynghori ar yr asesiad ffordd / rheilffordd cyn y Cyd-Bwylgor	Gwyrdd		Chwefror 2012	
90	Asesiad ffordd / rheilffordd i'w gyflwyno i'r Bwrdd Prosiect a'r Cyd-Bwylgor	Gwyrdd		Chwefror / Mawrth 2012	

**RISGIAU ALLWEDDOL** – Gweler eitem 6 ar yr agenda hon.

**Atodiad 1 – Amserlen Caffael Amlinellol**

Allwedd

Penderfyniad Cyd Bwyllgor	Penderfyniad awdurdodau partner unigol	Arolwg / Penderfyniad LIC
---------------------------	--	---------------------------

**Pwyntiau Penderfyniad Allweddol**

Cymal	Dyddiad Allweddol	Penderfyniad allweddol	Pwy
Cyd Bwyllgor – Ffordd /Rheilffordd	Mawrth 2012	Penderfyniad ffordd / rheilffordd	Cyd Bwyllgor (Swyddogion Arainnol i'w ymgynghori)
Cyd Bwyllgor - Dad-ddewis ISDS	21/06/2012	Dad-ddewis o un ymgweisiwr	Cyd Bwyllgor
Arolwg parodrwydd LIC	Medi to Hydref 2012	Ydy'r materion I gyd wedi ei ddatrys cyn cau deialog?	LIC
Cyd Bwyllgor i gymeradwyo cynigydd a ffefrir, Achos Busnes Terfynol a IAA2	Chwef 2013	Cynigydd a ffefrir, Achos Busnes Terfynol a IAA2	Cyd Bwyllgor
Awdurdodau unigol i gymeradwyo cynigydd a ffefrir, Achos Busnes Terfynol a IAA2 a rhoi caniatad i symyd ymlaen i wobrwyo'r cytundeb	Chwef i Mai 2013	Cynigydd a ffefrir, Achos Busnes Terfynol a IAA2 a rhoi caniatad i symyd ymlaen i wobrwyo'r cytundeb	Awdurdodau partner (Pwyllgor Gwaith, Cyngor Llawn, Pwyllgor Craffu ayb)
Arolwg "Gateway" 3 – Penderfyniad LIC (Cymeradwyaeth LIC o'r Achos Busnes Terfynol)	Mai i Mehefin 2013	Caniatau'r arian grant	LIC
Cyd Bwyllgor JC approval of Contract award	Awst 2013	Gwobrwyo'r cytundeb	Cyd Bwyllgor
Cais Cynllunio ar gyfer y prif gyfleuster	Gorff 2013		
Penderfyniad Cynllunio	Gorff 2013 i Mawrth 2014	Penderfyniad Cynllunio	Pwyllgor(au) cynllunio priodol o fewn y awdurdod(au) partner



# PTGGGC

Prosiect Trin Gwastraff Gweddilliol Gogledd Cymru

## EITEM AGENDA RHIF: 6

**ADRODDIAD I: CYD BWYLLGOR PTGGGC**

**DYDDIAD: 6 HYDREF 2011**

**ADRODDIAD GAN: Y CYFARWYDDWR PROSIECT**

**PWNC: : ADRODDIAD Y GOFRESTR RISG**

### 1. PWRPAS YR ADRODDIAD

- 1.1. Mae aelodau o Gyd Bwyllgor NWRWTP wedi gwneud cais i dderbyn diweddariad o'r gofrestr risg ym mhob cyfarfod o'r Cyd Bwyllgor.
- 1.2. Bydd yr adroddiad hwn yn tynnu sylw at rai o'r diwygiadau i'r gofrestr risg sydd wedi'u gwneud i adlewyrchu'r ddealltwriaeth bresennol o risgiau a'r mesurau lliniaru sydd yn eu lle.

### 2. CEFNDIR

- 2.1. Bydd angen diweddaru'r Gofrestr Risg yn barhaus drwy gydol y prosiect.

### 3. YSTYRIAETHAU

- 3.1. Mae un risg ychwanegol wedi ei adnabod yn y cyfnod adrodd yma.
  - PS 12 (Cynllunio a Chaniatau). Mae'r cyhoeddiad ddiweddar o'r Cynllun Sector Farchnadoedd, Isadeiledd a Chasgliadau gan LIC wedi arwain at ansicrwydd am statws y Cynllun Gwastraff Rhanbarthol sydd yn bodoli ar hyn o bryd. Mae'r bosib y gellir rhoi bwysau îs ar y Cynllun Gwastraff Rhanbarthol wrth benderfynnu ar gais cynllunio ar gyfer cyfleusterau gwastraff os yw'r ansicrwydd dros ei statws yn parhau. Mae'r Tîm Prosiect â'r Tîm Cynllunio Gwastraff Rhanbarthol Gogledd Cymru wedi bod yn trafod y mater gyda LIC i sicrhau nad yw'r fersiwn trefynnol o'r Cynllun Sector Farchnadoedd, Isadeiledd a Chasgliadau yn gadael "gwactod cynllunio".
- 3.2. Mae newid i risg F2 (Ariannol) yn y cyfnod hon (oediad yn y broses caffael yn arwain at gostau caffael uwch). Mae hyn oherwydd cais gan ymgeiswyr am estyniad i'r amserlen ISDS (tua 5 mis). Mae'r amserlen newydd dal o fewn y sensitifrwydd ofewn yr Achos Busnes Amlinellol o 12 mis o oedi i'r.
- 3.3. Mae'r 9 risg Uchaf (ar ôl gosod rheolaethau yn eu lle) yn cael eu dangos yn atodiad 1.
- 3.4. Risg TB4 wedi ei gau gan ei fod yn ail adrodd F2
- 3.5. Dangosir y newidiadau yn y cyfnod hwn yn atodiad 2



**PTGGGC**

Prosiect Trin Gwastraff Gweddilliol Gogledd Cymru

3.6. Bydd y gofrestr risg yn parhau i gael ei hadolygu gan y Cyfarwyddwr Prosiect a'i hadrodd i'r Cyd Bwyllgor mewn cyfarfodydd yn y dyfodol.

#### **4. ARGYMHELLION**

4.1. Bod y Cyd Bwyllgor yn nodi diweddariad y gofrestr risg ar gyfer y prosiect.

#### **5.00 GOBLYGIADAU ARIANNOL**

5.01 Amherthnasol

#### **5. EFFAITH GWRTH DLODI**

5.1. Dim

#### **6. EFFAITH AMGYLCHEDDOL**

6.1. Amherthnasol

#### **7. EFFAITH CYDRADDOLDEB**

7.1. Amherthnasol

#### **8. GOBLYGIADAU PERSONÉL**

8.1. Amherthnasol

#### **9. ANGEN YMGYNGHORIAD**

9.1. Amherthnasol

#### **10. YMGYNGHORIAD WEDI'I GYNNAL**

10.1. Amherthnasol

#### **DEDDF LLYWODRAETH LEOL (MYNEDIAD AT WYBODAETH) 1985**

#### **Dogfennau cefndir:**

Dim

**Swyddog Cyswllt:** Stephen Penny NWRWTP



## Atodiad 1 Prif risgiau a materion (Coch)

ID	Risk / Issue (i.e.: Threat to the Project)	Consequence	Current Assessment			How the risk will be managed and controlled		Residual risk after			Impln Date	Review Date	Additional explanatory notes
			Impact	L'hood	Overall	Already in Place	Not in Place (Proposed)	Impact	L'hood	Overall			
<b>Policy &amp; regulatory Risk – Change in WG objectives / regulations</b>													
PO1	WG changes financial support available for residual waste treatment projects due to WG affordability / budgetary constraints in the current economic climate	Residual waste treatment projects become less affordable for partnership and each partner authority	5	4	20	Project Team to monitor WG positions in terms of budget availability and lobby at ministerial level if there are indications that proposed funding is to be reduced		5	3	15	Ongoing	Nov-10	
PO2	WG Environmental policy and objectives change	Project is now inappropriate	4	5	20	Keep in close contact with WG to ensure potential policy changes that may impact on the project are identified early. Project team develop a partnership consultation response (for approval by the PB and Joint Committee) highlighting the potential impact of such a target on the project and to ensure WG addresses how any such target is related to potential household numbers of population growth rates that authorities may be subject to in future.		4	4	16	Ongoing	Feb-11	WG have indicated in the final Municipal Sector Plan (MSP) that they may adopt a waste minimisation target for MSW with a negative growth rate (reduction) of -1.2% pa. The WG MSP does not take any account of individual or partner authority HH or population growth rates. The Partnership has however received guidance from WG that the Partnership is free to make its own assessments about future waste arisings and as a result planning risk is now moderated.
PO4	Change in legislation or guidance either at European, National or Regional/Local level	Could require revisit of preferred solution, possible termination of project, excessive LAS compliance costs	3	5	15	Keep in close contact with WG to ensure potential policy changes that may impact on the project are identified early. Lobby WG and liaise with W/LGA on this issue.		3	4	12	Ongoing	Sep-10	WG have now clarified the position on use of IBA (Bottom ash) so the likelihood of policy change in relation to this has reduced. However recent sector plan consultations have raised the potential for the introduction of a tax on waste to energy. The Project team one of a number of options that WG may consider. If WG were to introduce such tax the financial impacts cannot be determined at this point but could potentially be considerable. (dependant on whether this would apply to household waste or just to C&I wastes). To be prudent the impact assement has been increased from 3 to 4 to reflect this uncertainty. The Project team have submitted a joint letter in conjunction with project green to WG. The Project team are now awaiting final publication of the Collections and Infrastructure Plan.



## Atodiad 2 Newidiadau yn y cyfnod hwn

ID	Risk / Issue (i.e.: Threat to the Project)	Consequence	Current Assessment			How the risk will be managed and controlled		Residual risk after			Impln Date	Review Date	Additional explanatory notes
			Impact	L'hood	Overall	Already in Place	Not in Place (Proposed)	Impact	L'hood	Overall			
<b>Communication &amp; stakeholders – failure to proactively engage with key stake holders leading to delays and lack of public support for the proposed solution.</b>													
CO4	Pressure from lobby groups/public against the preferred solution and location.	Alternative solution/site has to be sought, increased project development costs, delays to project delivery programme, excessive LAS costs,	4	5	20		Project team will ensure an adequate stakeholder engagement and communications plan in place. Alternative site work will continue during early stages of procurement process.	4	3	12	Ongoing	Sep-10	
<b>Procurement Strategy and Process</b>													
P13	Technological solutions offered are not commissionable within LAS infraction timescales	LA' s face infraction fines for additional landfill above allowance	4	4	16	OBC modelling has shown that each partner authority can meet LAS allowances if they increase "front end" recycling and composting" and the project is delivered to timetable. Any underperformance in this "front end" recycling and composting are outside the scope of this project and any	Procurement process to ensure that is delivered in timely manner with the risk of late delivery of the residual waste treatment service minimised.	4	3	12	Ongoing	Sep-10	
<b>Planning and permitting –ability to secure successful planning and permitting outcome for solution</b>													
PS5	Suitable sites are not in council ownership to support development of the solution	Project delayed whilst suitable sites are secured	5	3	15	Project team are identifying sites that could be suitable for location of both the waste transfer stations and residual waste treatment facility(s)	Commence negotiations with land owners of (further) additional sites identified as potentially suitable for location of facilities with the aim of securing	5	3	15	Ongoing	Sep-10	
PS14	The recent issue of the draft Collections, Infrastructure and Markets Sector Plan (CIM) by WG has led to uncertainty as to the status of the existing Regional Waste Plan (RWP). Thus the RWP may be given reduced weight in determination of a planning application for waste facilities. A policy vacuum may therefore exist if this is not addressed by WG.	Unsuccessful planning application	4	4	16	Project team and north wales regional waste planning team engaging with WG on this issue to ensure that the final issued version of Collections, Infrastructure and Markets Sector Plan (CIM) does not leave a planning "policy vacuum".		4	3	12	Ongoing	Sep-11	WG's published draft Collections, Infrastructure and Markets Sector Plan (CIM) indicates that RWP's will be replaced but with no indication as to timetable for replacement.





## Atodiad 2 Newidiadau yn y cyfnod hwn

ID	Risk / Issue (i.e.: Threat to the Project)	Consequence	Current Assessment			How the risk will be managed and controlled		Residual risk after			Impln Date	Review Date	Additional explanatory notes
			Impact	L'hood	Overall	Already in Place	Not in Place (Proposed)	Impact	L'hood	Overall			
<b>Wastes</b>													
W3	Composition of waste is different from that anticipated (poor data, policy changes, changes in collection practices)	Performance is below required level, excessive LAS compliance costs	3	5	15		Waste composition to be monitored during procurement and data shared at Competitive Dialogue to inform solution. All Wales Waste composition analysis being delivered by WG through WRAP. Initial work commencing in June 09. Performance of technology solution will be tested and understood as part of the procurement process to identify	3	4	12	Ongoing	Sep-10	Technology specific. EfW less sensitive to waste compositional change.
<b>Performance</b>													
PE1	Market/outlet is not available for outputs from the facility(s)	Increased project operational costs, increase in demand for landfill void	4	4	16		Ensure market deliverability demonstrated as part of procurement evaluation process.	4	3	12	Ongoing	Sep-10	Electricity sound, ash uncertain. Project and market saturation dependant.



# NWRWTP

North Wales Residual Waste Treatment Project

## AGENDA ITEM NO: 7

**REPORT TO: NWRWTP JOINT COMMITTEE**

**DATE: 6 OCTOBER 2011**

**REPORT BY: PROJECT MANAGER**

**SUBJECT: COMMUNICATIONS UPDATE**

### **1. PURPOSE OF REPORT**

- 1.1. To update the NWRWTP Joint Committee on communication matters concerning the North Wales Residual Waste Treatment Project (NWRWTP).

### **2. BACKGROUND**

- 2.1. The Joint Committee has requested regular updates on communication matters relating to the NWRWTP. This report provides an update on progress to date.

### **3. CONSIDERATIONS**

#### **3.1. Consultation Exercise - Summary**

The consultation exercise has been on going since the Member sessions were held in June 2011.

The closing date for consultation responses was Friday 23<sup>rd</sup> September, however the Project Team are including responses included for two weeks following this date in order to include as many responses as possible in the results. This was advertised in a press release that was issued on the 16 September 2011.

This means that a full report on the results of the consultation process will follow this report, however it was felt that an early indication of the results would be of benefit to the Joint Committee, therefore please note that the information below is an early indication and a summary of the results thus far only.

Below is a brief list of the activities that have taken place:-

- Two Member sessions were held (one “west” in Bangor, and one “east” in St Asaph)
- “Drop in” sessions at each of the five partner authorities (where members of the public were able to have an informal discussion about the project)
- Community Group sessions where various community groups etc were invited to attend a meeting to discuss the project and the consultation.



# NWRWTP

North Wales Residual Waste Treatment Project

- 2 interest group sessions where environmental / interest groups were invited to discuss the project (1 x east and 1 x west).
- The consultation questionnaire can be complete on line, and project website has a consultation page.
- The consultation has been advertised internally within the five partner authorities, including booklets distributed to Council Offices, libraries etc.
- A telephone survey of the consultation questionnaire commissioned of 1,000 residents of the partnership area.

### Member sessions

Two Member sessions were held on the 17<sup>th</sup> and 28<sup>th</sup> of June 2011. One “west” session in Bangor (Parc Menai), and one “east” session in St Asaph (Optic).

General feedback from the sessions is that they were a success, in particular the aspect of the Members of partner authorities meeting together. Appendix 3 shows the attendance for both sessions, followed by a brief list of the questions that were asked during the sessions.

### Drop in sessions

These were advertised in the local press / media through an advert in all the local press across the five authorities, together with a series of press releases. They were also advertised on the project website. As expected, turnout was low at the authorities where sites have not been mentioned as potentially hosting a facility.

- Conwy - 13
- Gwynedd (Dolgellau and Bangor) - 6
- Anglesey - 23
- Denbigh - 6
- Flintshire - 49 (27 at St David's Park, 22 at Connah's Quay Town Council)

Total attendance = 97

Below is a brief summary of the discussions held at the sessions

- Most of the discussions held were detailed, with some lasting over an hour. These were valuable and in depth discussions.
- The vast majority left the sessions happier than when they arrived, although there was a number that even after the discussions were against certain proposals (e.g. EfW at Anglesey or EfW at Deeside Industrial Park)
- In Gwynedd, Anglesey, Conwy and Denbighshire the vast majority of attendees were supportive of the project, and wanted to know more about it.
- In Flintshire, there was a greater concern about the possibility of an “incinerator at Deeside”, mainly centred around health effects. There is a lack of trust in the permitting and licensing regime from those that were opposed.
- It should be noted, though, that while a good number of the Flintshire drop in sessions' attendees had concerns, it was by no means universal, and indeed a good proportion were either



# NWRWTP

North Wales Residual Waste Treatment Project

supportive, or could recognise the arguments being made for both need, and why the site was being considered.

- It did not come across at any of the sessions that there is a groundswell of opposition to the project.

### Community Group sessions

The Community Group and interest group sessions were not well attended at all, with some sessions with one or two attendees. This is despite follow up calls to the invitees. In total, 12 people attended 5 sessions.

Overall, however, feedback was very positive at those sessions, with nearly all attendees supportive of the project. The sessions did, however, provide a good opportunity for detailed discussion, and also provided vital contacts for further consultation and engagement in the future.

### Summary of various “drop in” and community group sessions

Overall, whilst the attendance at some of the various sessions was disappointing, the project team has learnt a great deal from the sessions, and has had detailed discussions with a good number of residents, and opened up further avenues for engaging (more community groups identified etc).

The process has also highlighted the importance of a pro active engagement campaign throughout the procurement process, and it is clear that an informal detailed discussion with a resident has a far greater effect than more formal communications avenues (e.g. press releases etc)

### 3.2. Press Coverage

Face to face briefings were given to some of the local press during July in order to advertise the consultation process, and three press releases were issued during August and September advertising the drop in sessions and the closing date for consultation responses. There was reasonable press / media coverage during the consultation process and all the local press / media ran at least one story of some sort advertising the sessions (including BBC news website, Real Radio interview etc). Some ran a number of stories on the consultation. See appendix 2 below for some examples of the coverage.

### 3.3. Consultation Questionnaire – indication of results

In appendix 1 below are some graphs showing an early indication of the results thus far. The number of consultation responses received thus far is 305 (162 booklets, 143 via the on line questionnaire).

### 3.4. Communication and Engagement planning

The Project Team have arranged a meeting with technical and communication advisors on 21 October 2011 to plan communication and



# NWRWTP

North Wales Residual Waste Treatment Project

engagement going forward for the following 12 months. This will be put before the Joint Committee for approval once it is finalised.

#### **4. RECOMMENDATIONS**

4.1. To note the content of this update report.

#### **5. FINANCIAL IMPLICATIONS**

5.1. Not applicable.

#### **6. ANTI-POVERTY IMPACT**

6.1. Not applicable.

#### **7. ENVIRONMENTAL IMPACT**

7.1. Not applicable.

#### **8. EQUALITIES IMPACT**

8.1. Not applicable .

#### **9. PERSONNEL IMPLICATIONS**

9.1. Not applicable.

#### **10. CONSULTATION REQUIRED**

10.1. See above.

#### **11. CONSULTATION UNDERTAKEN**

11.1. Not applicable.

#### **LOCAL GOVERNMENT ACCESS TO INFORMATION ACT 1985**



##### **Background Documents:**

None

**Contact Officer:** Steffan Owen NWRWTP



## Appendix 1 Graphs of results of consultation process thus far

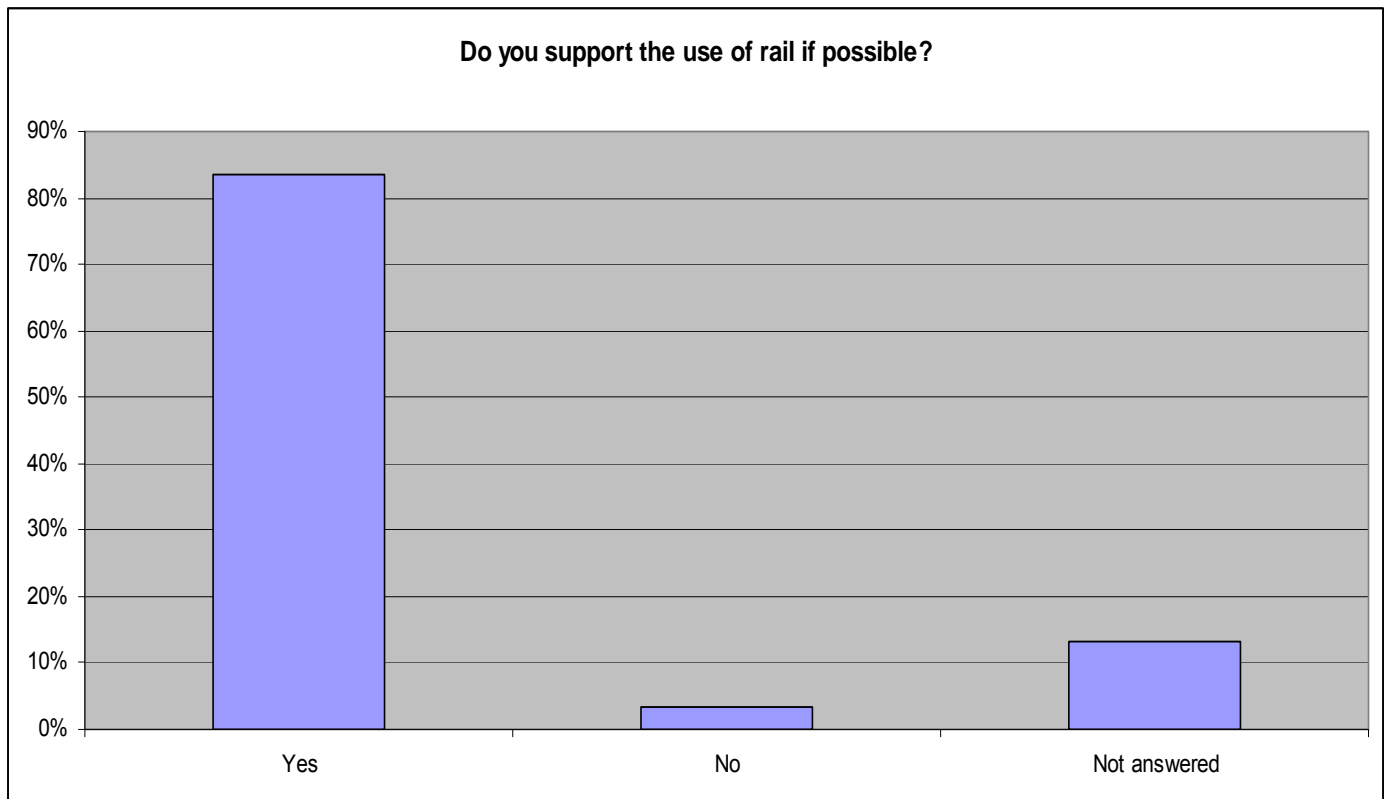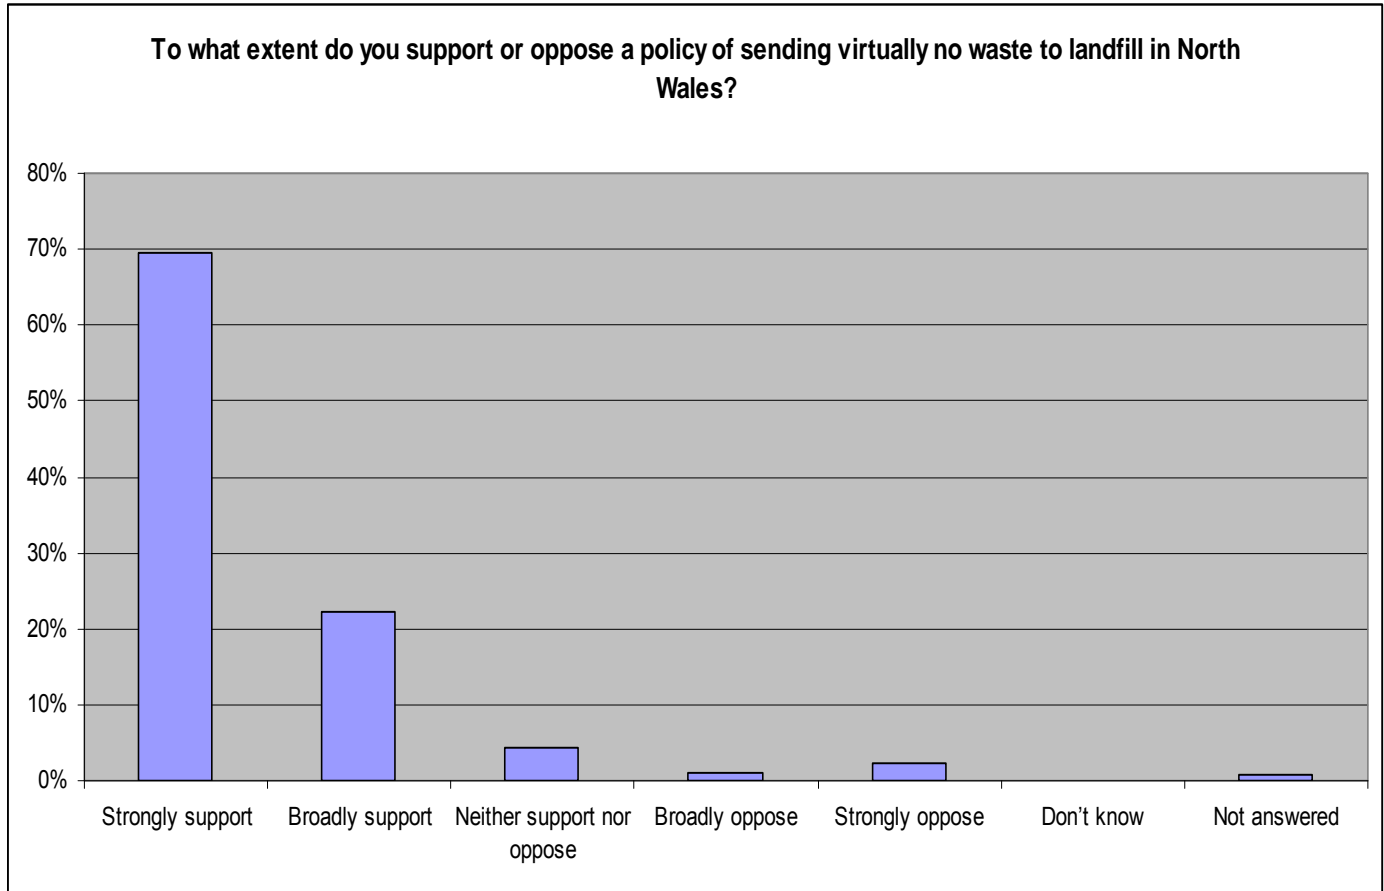





# NWRWTP

North Wales Residual Waste Treatment Project

## To what extent do you support the use of rail is possible?

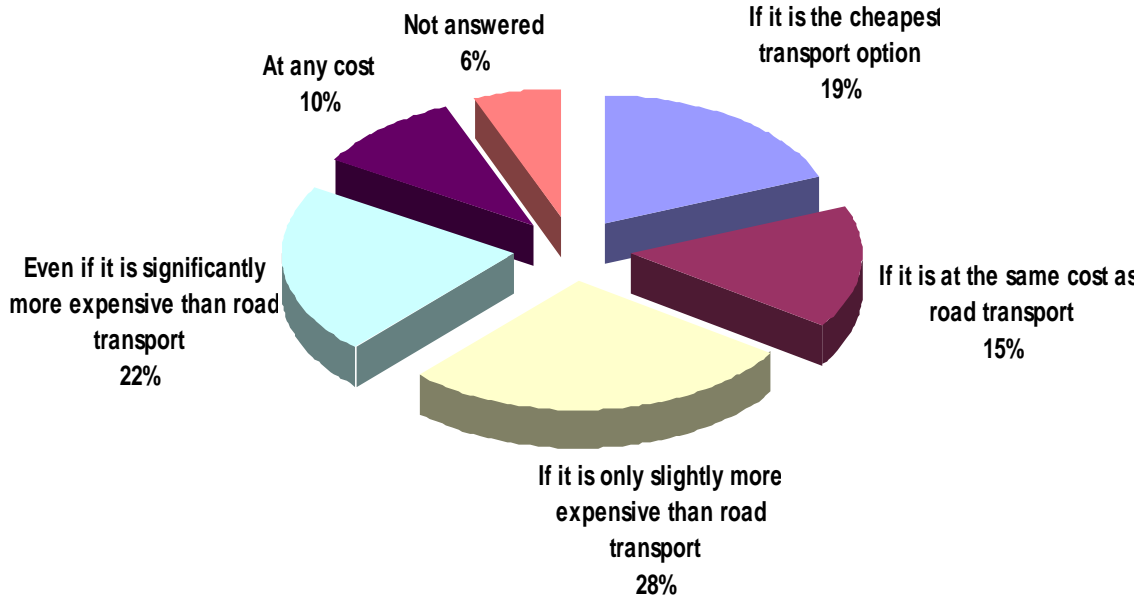

## Where the waste will come from

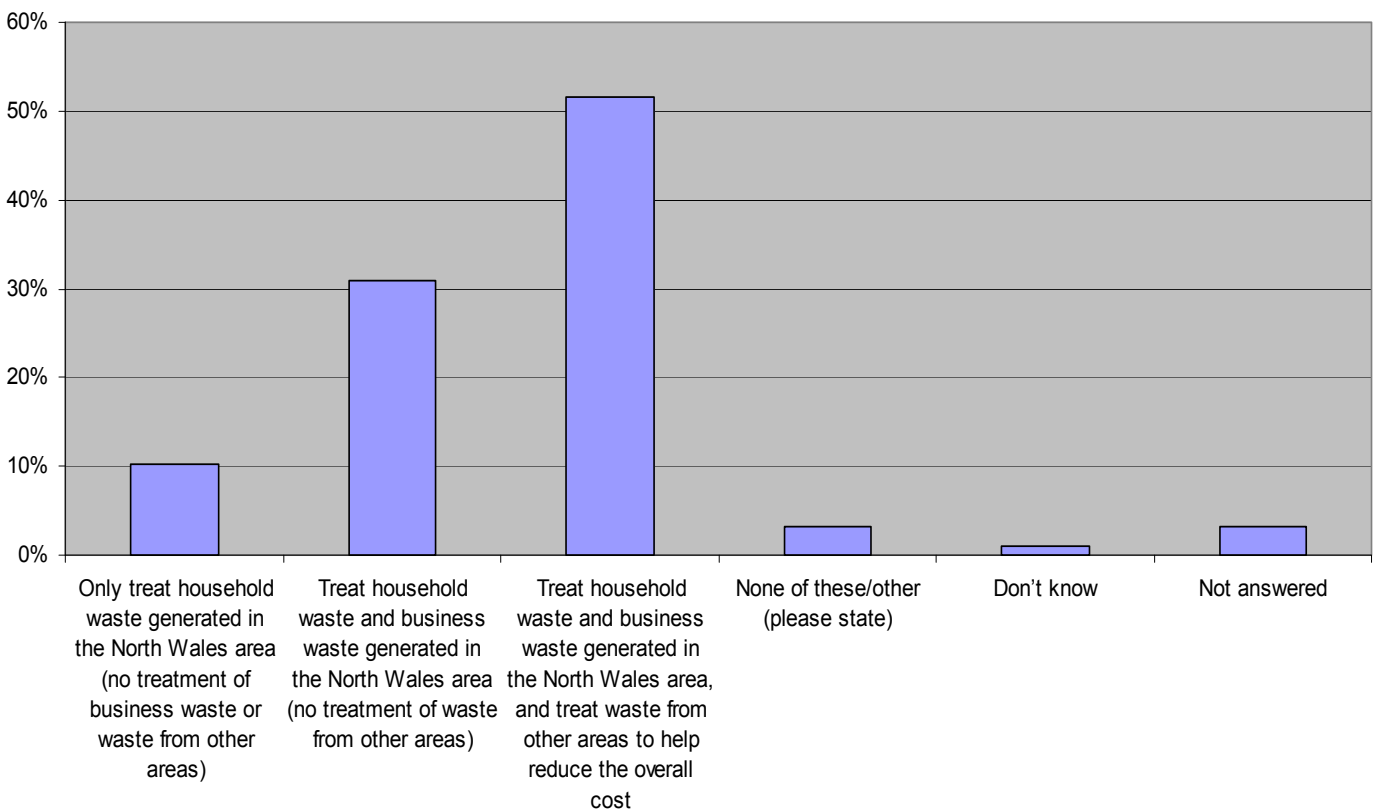



## Appendix 2 – Examples of some of the press coverage

# County residents urged to have say on waste incinerator plans

### RESIDENTS are being urged to have their say on controversial plans which could see an incinerator built on Deeside.

A consultation was launched this week into the Welsh Government's £142.7 million North Wales Residual Waste Treatment Project (NWRWTP) set up to manage waste across five councils in the region.

The prospects of an incinerator on Deeside have been described as a "real threat".

An outline business case presented by project bosses caused anger when it gave Deeside Industrial Estate as the only example of a possible location for an incinerator to handle waste which cannot be recycled.

Now people in Flintshire, Denbighshire, Anglesey,

Gwynedd and Conwy are being asked for their views on the waste treatment facility.

Steffan Owen, project manager for NWRWTP, said: "We have created a leaflet and want to inform people about the project.

"There are questions in the leaflet and the answers given will inform the direction in which we proceed."

Questions include asking people for their views on recycling, on transporting waste by rail and from how far away the new facility should take waste.

Connah's Quay Central councillor Aaron Shotton said the Health Protection Agency was researching the link between infant mortality and incinerator sites in England.

He said: "Given the health effects have not been disproved, I would still urge Flintshire Council to rule out incineration and rule out

Deeside as an option.

"The people of Deeside do not want this and it is important they understand an incinerator on Deeside is a very real threat.

"There is a real and present danger," and Cllr Shotton urged residents to join a campaign against a site in Deeside.

Residents are also asked for their views on benefits the project could bring to the area, such as employment opportunities and the ability to use heat from treating the waste as a power source.

Anxious councillors opposed to an incinerator on Deeside are urging people to fill in the questionnaire.

Connah's Quay councillor Bernie Attridge said: "I'm entirely opposed to an incinerator on Deeside and I will campaign against it.

"I was always told by officers taking this project forward they were energy neutral, but the shortlisted three all specialise in getting energy from waste and that means incinerators. I know a decision has not been made yet but the longer this process goes on the more concerned I am for Deeside."

But project bosses insist Deeside is not confirmed as the definite site. "The document had to name a potential site and potential technology," said Mr Owen. "We put Deeside in because it's

a potential site."

Mr Owen's colleague John Twitche said: "We couldn't just name a site in make believe, it had to be suitable.

"The land is owned by Flintshire Council and it is also in the development plan for suitable development.

"What might be built and where it might be built is not yet determined."

Mr Owen said bidders are welcome to submit other potential sites in their plans.

The project team has also identified a potential site in Anglesey and is in talks with Anglesey Aluminium to finalise an agreement to list their land as a possible location.

Consultation leaflets are available from today and feedback can also be given at [www.nwrwtp.org](http://www.nwrwtp.org).

Details of drop in sessions for the public, planned for later this summer, are still to be confirmed.

● **WHAT do you think about the project? Have your say at [www.leaderlive.co.uk](http://www.leaderlive.co.uk)**



■ Cllr Bernie Attridge.



■ Cllr Aaron Shotton.







# NWRWTP

North Wales Residual Waste Treatment Project

## Consultation begins on waste site

**PUBLIC consultation has begun over multi-million pound plans to process non-recyclable waste.**

Up to 150,000 tonnes of rubbish from five counties across North Wales could be dumped on Anglesey if the scheme gets the go-ahead.

Land belonging to Anglesey Aluminium Ltd has been earmarked as a possible location for an incinerator.

North Wales' five main councils have joined forces to create the region's largest joint local government

procurement project.

It represents an investment of up to £800m over its 25-year lifetime.

The partnership, called the North Wales Residual Waste Treatment Project (NWRWTP), has invited firms to draw up plans for

processing plants like incinerators to deal with waste currently put into landfill.

As well as Anglesey, a site in Deeside, Flintshire, has been identified prompting some concerns from people living nearby.



Anglesey Aluminium





# NWRWTP

North Wales Residual Waste Treatment Project

BBC News - Deeside waste incinerator consultation begins - Microsoft Internet Explorer provided by Flintshire County Council

http://www.bbc.co.uk/news/uk-wales-north-east-wales-14067745

File Edit View Favorites Tools Help

Wales Politics North West North East Mid South West South East

## NEWS NORTH EAST WALES

Home World UK England N.Ireland Scotland Wales Business Politics Health Education Sci/Environment Technology Entertainment & Arts

9 July 2011 Last updated at 10:05

### Deeside waste incinerator consultation begins

Public consultation has begun over multi million pound plans to process non-recyclable waste in north Wales.

Officials have invited firms to draw up plans for processing plants like incinerators to deal with waste currently put into landfill.

So far, two potential sites have been earmarked on Anglesey, Gwynedd, and in Deeside, Flintshire, prompting some concerns from people nearby.

Residents are now being given the opportunity to have their say.

North Wales' five main councils have joined forces to create the region's single largest joint local government procurement project.

It represents an investment of up to £800m over its 25-year lifetime.

Flintshire council is taking the lead among the group made up of authorities covering Anglesey, Gwynedd, Conwy, and Denbighshire.

The partnership is called the North Wales Residual Waste Treatment Project (NWRWTP).

Last year, they announced Deeside Industrial Estate could potentially be used as a site to locate an energy from waste incinerator.



The Welsh Government has agreed to put £142m into the project

#### Top Stories

- BAE confirms loss of 3,000 posts
- Miliband attacks 'fast buck' UK
- Dad's Army co-creator Croft dies **NEW**
- Knox no femme fatale, lawyer says
- Shares up on eurozone rescue hope

#### Features & Analysis

- Headphone generation**  
Has the iPod turned us all into anti-social people?
- Courtroom date**  
Michael Jackson's personal doctor set to face manslaughter charge
- Call centre relocation**  
Do people have a problem with Indian accents?
- Surgical slicing**  
The gloves are off in fight for NHS savings

#### Most Popular

Shared Read Video/Audio

Related Stories

- Jobs and tourism 'balance needed'
- Council discusses new waste plan

BBC News Wales Website - 9 July 2011

BBC News - £800m North Wales Residual Waste Treatment talks start - Microsoft Internet Explorer provided by Flintshire County C

http://www.bbc.co.uk/news/uk-wales-north-east-wales-14415802

File Edit View Favorites Tools Help

Wales Politics North West North East Mid South West South East

5 August 2011 Last updated at 07:52

### £800m North Wales Residual Waste Treatment talks start

Public consultation is starting over plans to process non-recyclable waste in north Wales, possibly building an incineration plant.

Two sites in Deeside and Anglesey have been earmarked in the £800m project.

Officials say nothing has been finalised and all ideas are being considered.

They are holding talks with residents across the region, starting at Holyhead on Friday.

North Wales' five main councils have joined forces and invited firms to draw up plans for processing plants **2011-09-27 (Press ENTER to Insert)** like incinerators to deal with waste currently put into landfill.

They expect it will process more than 150,000 tonnes of waste a year in a project costing an estimated £800m over 25 years.

Flintshire council is taking the lead among the group made up of authorities covering Anglesey, Gwynedd, Conwy, and Denbighshire.


The partnership is called the North Wales Residual Waste Treatment Project (NWRWTP).

#### 'People against'

Councillor Eryl Williams, chair of the NWRWTP's joint committee, said the Welsh Government has set target of recycling 70% of household waste by 2025, and using landfill was no longer an option.

He told BBC Radio Wales "there are bound to be people against" plans put forward.

"People don't want things on their doorstep," he said.



The plan is to process 150,000 tonnes of non-recyclable waste a year

#### Top Stories

- BAE confirms loss of 3,000 posts
- Miliband attacks 'fast buck' UK
- Dad's Army co-creator Croft dies **NEW**
- Knox no femme fatale, lawyer says
- Shares up on eurozone rescue hope

#### Features & Analysis

- Headphone generation**  
Has the iPod turned us all into anti-social people?
- Courtroom date**  
Michael Jackson's personal doctor set to face manslaughter charge
- Call centre relocation**  
Do people have a problem with Indian accents?
- Surgical slicing**  
The gloves are off in fight for NHS savings

#### Most Popular

Shared Read Video/Audio

Daughter found after three years	1
Comedy creator David Croft dies	2
'Cover up', farmer tells Rihanna	3
MP's wife in bitter theft trial	4

#### Related Stories

- Next phase in £800m waste project
- Jobs and tourism 'balance needed'
- Council discusses new waste plan

#### PUBLIC MEETINGS

- ANGLESEY: Boston Centre Stage, Boston Street, Holyhead; 5 August, 14:00-19:00 BST and 6 August 10:00-16:00 BST



# NWRWTP

North Wales Residual Waste Treatment Project

## Appendix 3 – attendance at the June 2011 Member sessions, and a list of the questions asked at the sessions.

<b>Friday 17<sup>th</sup> June 2pm Ty Menai (Formerly Technium CAST) Parc Menai , Bangor</b>	<b>Attended ✓</b>
Cynghorydd RH Wyn Williams (G)	✓
Councillor Gail Hall (C)	✓
Councillor Robert Llewelyn Jones (A)	✓
Councillor Ioan Thomas (G)	✓
Councillor Eurfryn Davies (A)	✓
Councillor Goronwy Parry (A)	✓
Councillor Peter Rogers (A)	✓
Councillor Edward T Dogan	✓
Cynghorydd Eric M Jones (G)	✓
Cynghorydd Gwilym Williams (G)	✓
Councillor Ian Jenkins (C)	✓
Councillor Mike Rayner (C)	✓
Councillor Alwyn Gruffydd (G)	✓
Councillor John Wynn Jones (G)	✓



# NWRWTP

North Wales Residual Waste Treatment Project

<b>Tuesday 28<sup>th</sup> June 9.30am Optic Technium, St. Asaph</b>	<b>Attended ✓</b>
Councillor Carolyn Thomas (F)	✓
Councillor Jim Falshaw (F)	✓
Councillor Brian Cossey (C)	✓
Councillor Nancy Matthews (F)	✓
Councillor Huw Jones (D)	✓
Councillor Christine Jones (C)	✓
Councillor Eng. Klaus Armstrong-Braun (F)	✓
Councillor Christine Evans (D)	✓
Councillor Dave Mackie (F)	✓
Councillor Doreen Mackie (F)	✓
Councillor Susan Shotter (C)	✓
Councillor Dewi Owens (D)	✓
Councillor Eric Owen (F)	✓
Councillor Robin Baker (F)	✓
Councillor Mrs MC Doyle (C)	✓
Councillor William Knightly (C) (poss)	✓
Councillor Mike Priestley (C)	✓
Councillor Chris Bithell (F)	✓
Councillor Ronald Peacock (C)	✓
Councillor John Bevan (C)	✓
Councillor Geoff Corry (C)	✓
Councillor Andrew Hinchliff (C)	✓
Councillor Keith Marshall (G)	✓
Councillor Dennis Hutchinson (F)	✓
Councillor Aaron Shotton (F)	✓
Councillor David Cox (F)	✓
Councillor Raymond Hughes (F)	✓
Councillor Neville Phillips (F)	✓
Councillor Colin Legg (F)	✓
Councillor Gwilym Charles Evans (D)	✓
Councillor Cefyn Henry Williams (D)	✓
Councillor Huw Jones (D)	✓
Councillor Michael John Eckersley (D)	✓
Councillor AM Khan (C) (poss)	✓
Councillor Grenville James (F)	✓
Councillor Bill Cowie (D)	✓
Councillor Ken Stone (D) – Town Council (Mayor of Kinmel Bay & Towyn)	✓



## **Questions Raised**

### **17 June 2011**

- What percentage of waste will be sent to recovery?
- Does this solve the landfill problem?
- Is there enough waste for the facility?
- How will the £600 million be allocated across the local authorities, will there be a penalty if we miss the minimum tonnage? Will we have to divert recycling to energy recovery?
- How much energy will it produce and what are the emissions?
- Keep Wales tidy - take it to England! But I do understand, there is economic benefit in doing it here, but why can't we do it ourselves, employ a Welsh company?
- What are the problems with the gateway to the EU, will we see waste imported?
- Corks used to be made out of cork, now they are not which is bad for cork trees. Now we have this waste that we didn't have – what can be done?
- Will it all be taken by rail? e.g. Gwynedd
- Will there be a mobile visitor centre?
- Are we creating something we don't need?

### **28 June 2011**

- From the seven bids received at ISOS, were there any alternatives to energy from waste?
- How can new technologies ever develop if we can't select one and back it?
- Has the timescale slipped?
- I have been bombarded by information from Friends of the Earth, are their claims correct?
- How sound is the technology and how tried and tested is it?
- Why not Mechanical Biological Treatment (MBT)?
- Will there be compensation if you don't fill the facility?
- Germany re-uses residual waste from energy from waste – will we?
- What happens if there is not enough waste?



# NWRWTP

North Wales Residual Waste Treatment Project

- What about legislation affecting commercial waste collectors, is it the same/are there targets?
- Public need to be convinced that we need this, they need information – what's being done?
- It's not really technology neutral, we were supposed to be technology neutral, are councillors finding out about this change in position when it's already too late?
- Where are the sites?
- Will it be transboundary? Will commercial waste come from outside Wales?
- What about Wrexham, will they be involved in this?
- Will people be happy to accept the facility near them?

FLINTSHIRE COUNTY COUNCIL

EXEMPT INFORMATION SHEET

---

COMMITTEE: NWRWTP Joint Committee

DATE: 6 October, 2011

AGENDA ITEM NO: 8

REPORT OF: Project Director

---

SUBJECT: Waste Flow Model Update

---

The Report on this item is NOT FOR PUBLICATION because of exempt information in accordance with the following section(s) or paragraph(s) of Schedule 12A of the Local Government Act 1972:

	<u>Para</u>	
Information relating to a particular individual *	12	[ ]
Information likely to reveal the identity of an individual *	13	[ ]
Information relating to financial/business affairs of a particular person * See Note 1	14	[✓]
Information relating to consultations/negotiations on labour relations matter *	15	[ ]
Legal professional privilege	16	[ ]
Information revealing the authority proposes to:		
(a) give a statutory notice or		
(b) make a statutory order/direction *	17	[ ]
Information on prevention/investigation/prosecution of crime *	18	[ ]
<u>For Standards Committee meetings only:</u>	<u>Sec</u>	
Information subject to obligations of confidentiality	18A	[ ]
Information relating to national security	18B	[ ]
The deliberations of a Standards Committee in reaching a finding	18C	[ ]
Confidential information which the Council is not permitted to disclose	100A	[ ]
	(3)	

**PLEASE TICK APPROPRIATE BOX**

\* Means exempt only if the public interest in maintaining the exemption outweighs the public interest in disclosing the information.

Note 1: Information is not exempt under paragraph 14 if such information is required to be registered under Companies Act 1985, the Friendly Societies Acts of 1974 and 1992, the Industrial and Provident Societies Act 1965 to 1978, the Building Societies Act 1986 or the Charities Act 1993.

**SCHEDULE 12A LOCAL GOVERNMENT ACT 1972  
EXEMPTION FROM DISCLOSURE OF DOCUMENTS**

**REPORT:** Waste Flow Model Update

**AUTHOR:** Project Director

**MEETING AND DATE OF MEETING:** NWRWTP Joint Committee  
6 October, 2011

I have considered grounds for exemption of information contained in the report referred to above and make the following recommendation to the Proper Officer:-

**Exemptions applying to the report:**

Paragraph 14

**Factors in favour of disclosure:**

Transparency

**Prejudice which would result if the information were disclosed:**

The report contains information which if disclosed at the present time could prejudice a fair bidding process.

**My view on the public interest test is as follows:**


On balance, at the present time it is not in the public interest to make the information publicly available.

**Recommended decision on exemption from disclosure:**

Exempt from disclosure

**Date:** 28 September, 2011


**Signed:**



**Post:** Team Manager – Committee Services

---

I accept the recommendation made above.



---

Proper Officer

Date: 28 September, 2011
